

Human Resource Plan

furlink

Humabon Place, Magallanes Village

Makati City, Metro Manila, 1232

April 2026

Table of Contents

1. Introduction3

2. Roles and Responsibilities.....3

3.Project Organizational Charts5

4. Staffing Management6

Sponsor Acceptance8

1. Introduction

Human resources management is a critical component of the furlink project. This plan serves as a tool to aid in the management of human resource activities from development through to User Acceptance Testing (UAT) and final deployment. Roles and responsibilities of team members throughout the project

The furlink Human Resource Plan includes:

- Roles and Responsibilities: Clear definitions for team members.
- Project Organization Charts: Visualizing hierarchy and task assignments.
- Staffing management plan to include:
 - a. How resources will be acquired
 - b. Timeline for resources/skill sets
 - c. Training required to develop skills
 - d. How performance reviews will be conducted
 - e. Recognition and rewards system

The goal is to ensure the project has the necessary technical skills (React.js, Supabase, QA testing) and that team activities are effectively managed to meet the project's social impact goals.

2. Roles and Responsibilities

The roles and responsibilities for the Software Upgrade Project are essential to project success. All team members must clearly understand their roles and responsibilities in order to successfully perform their portion of the project. The following project team roles and responsibilities have been established:

Project Manager (PM), (1 position): responsible for the overall success of the Software Upgrade Project. The PM must authorize and approve all project expenditures. The PM is also responsible for approving that work activities meet established acceptability criteria and fall within acceptable variances. The PM will be responsible for reporting project status in accordance with the communications management plan. The PM will evaluate the performance of all project team members and communicate their performance to functional managers. The PM is also responsible for acquiring human resources for the

project through coordination with functional managers. The PM must possess the following skills: leadership/management, budgeting, scheduling, and effective communication.

Developer (LD): The Developers are accountable for the end-to-end technical architecture and construction of the furlink web application, possessing the authority to make critical decisions regarding the tech stack, library selections, and database schema design. Primary responsibilities include leading the coding of the Vite frontend to ensure seamless booking experience and architecting the Supabase backend with robust security protocols and real-time data triggers. This role requires a high degree of technical competency in JavaScript, CSS, and PostgreSQL to ensure the platform is scalable, high-performing, and maintains structural integrity across various user devices and browser environments.

QA Tester / Intern (QA): The QA Tester focuses on ensuring the reliability and user-friendliness of the platform by developing comprehensive test plans that cover both manual functional testing and automated regression suites. This role holds the authority to flag critical bugs that could delay a release, ensuring that the software is thoroughly validated before it reaches the end user. Responsibilities include documenting all identified issues, verifying technical fixes, and facilitating User Acceptance Testing (UAT) sessions with actual pet groomers to measure the platform's ease of use. Success in this role requires strong analytical skills and a deep understanding of the Software Testing Life Cycle (STLC) to prevent data errors or UI failures.

Release Manager (RM): The Release Manager bridges the gap between development and production, holding the authority to approve deployments based on the readiness of the hosting environment and the stability of the code. This role is responsible for managing the continuous integration and deployment pipeline, monitoring system uptime, and ensuring that security measures like SSL certificates and environment variables are correctly configured. By coordinating update windows to minimize disruption for active users and

maintaining the server infrastructure, the Release Manager ensures a smooth "go-live" process and long-term operational stability for the furlink platform.

3.Project Organizational Charts

The following RACI chart shows the relationship between project tasks and team members. Any proposed changes to project responsibilities must be reviewed and approved by the project manager. Changes will be proposed in accordance with the project's change control process. As changes are made all project documents will be updated and redistributed accordingly.

	Project Manager	Developers	QA Tester	Release Manager
Requirements Gathering	A	R	C	I
Database & Schema Design	A	R	I	C
Frontend & Backend Coding	I	R/A	C	I
Software & Unit Testing	A	C	R	I
User Acceptance Testing (UAT)	A	I	R	C
Environment Preparation	A	C	I	R
Final Implementation/Release	A	C	I	R

Key:

R – Responsible for completing the work

A – Accountable for ensuring task completion/sign off

C – Consulted before any decisions are made

I – Informed of when an action/decision has been made


4. Staffing Management

Staff Acquisition:

Project staff for furlink consists of internal student resources. The Project Manager identifies and assigns resources based on the technical requirements of the platform. All resources will work remotely or from the designated campus workspace.

Resource Calendars:

The PROJMAN Course will last for four months. All resources are required before the project can begin. The resource histogram below illustrates that the resource histogram below illustrates that the Project Manager, Developers, QA Tester, and Release Manager will all perform work for 40 hours per month from March to June.

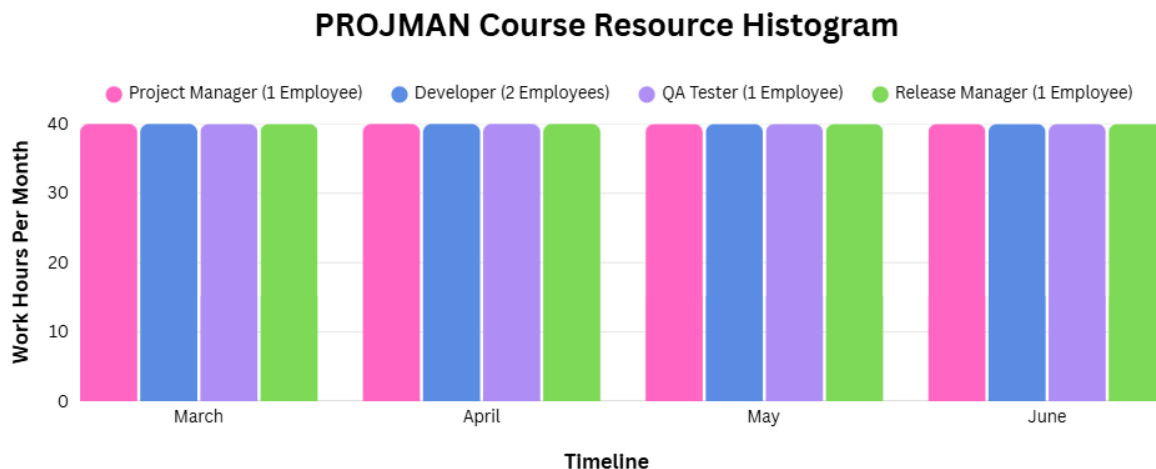

Training:

As the team is proficient in the chosen tech stack (Vite/Node.js/Supabase), no formal training is scheduled. If truly needed, the team will access free training and guides through the internet and other resources.

Performance Reviews:

The PM will evaluate team members based on the successful completion of "sprints" and the quality of code/documentation produced. Feedback will be provided during project status meetings.

Recognition and Rewards:

To maintain motivation throughout the development of the pet grooming platform:

- **Completion Event:** A "Launch Party" for the team upon the successful first booking on the platform.

Sponsor Acceptance

Approved by the Project Sponsor:



Manuel R. Doria Jr.

Project Sponsor Representative

Date: April 7, 2026
