



ANDAYA, DORIA, PINEDA, SALTING

1.0 INITIATION PHASE

PROJECT CHARTER

Feliz
Angelica
Salting



- furlink aims to innovate the way local pet grooming services are booked and managed.
- Target users include dog and cat owners and small to medium enterprise pet grooming shops
- furlink's objective is to reduce scheduling conflicts, improve SP visibility, streamline booking journey, and provide business insights for SP
- Target timeline is to successfully deploy versions v1.0 through v2.1 between April and August 2026.



PROJECT CHARTER

Feliz
Angelica
Salting



MILESTONES

Milestones	Date
Capstone 2 Kickoff	March 7, 2026
Initial Release to Service Provider	April 20, 2026
<u>furlink</u> v1.0 Optimization	April 24, 2026
Enhancement of Core Booking Modules	April 27, 2026-May 4, 2026
<u>furlink</u> v1.1 Enhanced Stability Release	May 7, 2026
Development of AI Booking Assistant	June 17, 2026-July 17, 2026
Development of Payment Gateway	July 22, 2026-July 29, 2026
System and Integration Testing	July 30, 2026-August 4, 2026
<u>furlink</u> v2.0 Release	August 5, 2026
User Acceptance Testing & Fixes	August 6, 2026-August 31, 2026
Solution Release <u>furlink</u> v2.1	August 31, 2026
Project Completion	October 1, 2026
Project Closure & Documentation Handoff	October 17, 2026

BUSINESS CASE

Feliz
Angelica
Salting



PROBLEMS

- Local pet grooming shops rely on decentralized, manual booking methods (notebooks, whiteboards, SMS, Facebook Messenger).
- High rates of missed appointments, recurring double-booking incidents (affecting 33% of businesses), and lack of performance tracking tools.

BUSINESS CASE

Feliz
Angelica
Salting



SOLUTION

- Transitioning shops from manual tracking to a unified, web-based platform.
- Real-time calendar synchronization to completely eliminate double bookings.
- A conversational AI assistant to simplify booking and ensure accurate service expectations.
- A dedicated dashboard for tracking monthly revenue, customer feedback, and booking trends.

BUSINESS CASE

Feliz
Angelica
Salting



COST-BENEFIT SUMMARY

Action	Action Type	Description	First Year costs
Labor Costs	Cost	Compensation for the 4-member core team over the 7-month development	₱560,000.00
Fixed Costs	Cost	Cloud infrastructure, domain registration, and project overhead required	₱23,500.00
Contingency Reserve	Cost	Baseline reserve fund allocated to mitigate unforeseen risks or schedule	₱58,350.00
Mitigation of "No-Shows"	Savings	1 shop preventing 1 missed ₱1,000 appt/week via PayMongo downpayments.	-₱32,000.00
Increased Revenue	Savings	1 shop gaining 1 new client/week.	-₱32,000.00
Net First Year Impact		(Total Project Cost: ₱705,850 - Total Year 1 Savings:	₱64,000.00

PROJECT BRIEF

Michelle
Reina
Pineda



SUCCESS CRITERIA

Reduce Booking Conflicts: Service providers experience no double-bookings during the first three months.

Provider Onboarding: Successfully verify and onboard at least one local service provider by July 20, 2026.

Visibility Boost: 100% of onboarded providers have an active, functional SEO profile dashboard.

Process Automation: Automate 50% of data entry for bookings to eliminate manual errors.

Request Accuracy: Achieve 95% accuracy in platform understanding of user booking requests.


Payment Efficiency: Instant, error-free delivery of PayMongo links upon booking confirmation.

Business Insights: Integrate a full analytics dashboard for tracking sales and feedback by August 3, 2026.

UAT Approval: Complete User Acceptance Testing with all critical bugs resolved by August 31, 2026.

TARGET AUDIENCE

Dog/Cat Owners and Pet Service Providers

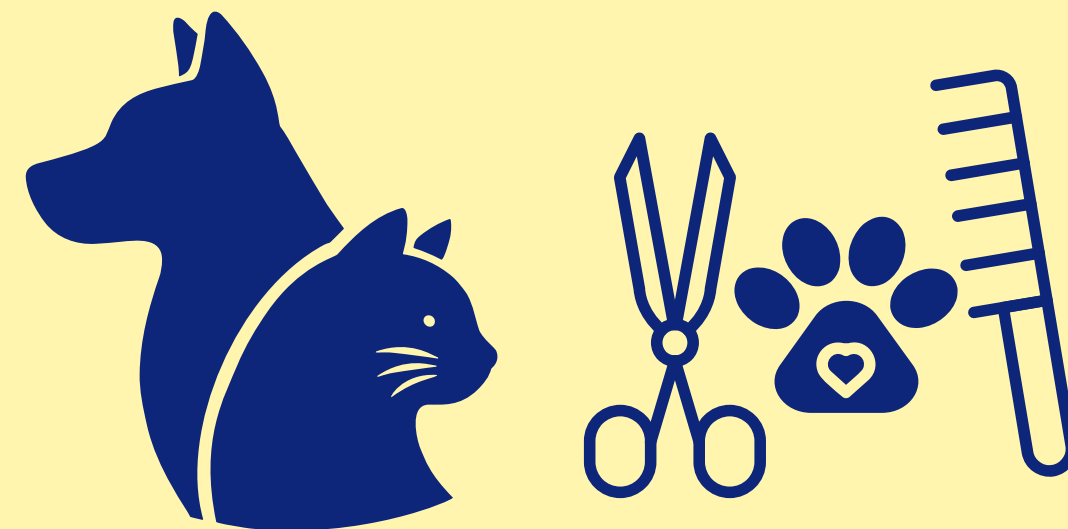

STAKEHOLDER MANAGEMENT STRATEGY


Atasha
Frances
Gayle Doria



DISCOVERY METHODOLOGY



Market
Research

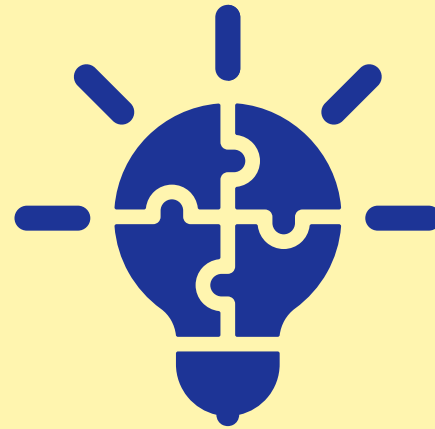

Brainstorming



Interview

STAKEHOLDER MANAGEMENT STRATEGY

Atasha
Frances
Gayle Doria



Stakeholder Inclusion Criteria

1. Is the person or their organization directly or indirectly affected by the furlink platform?
2. Does the person or their organization hold a position from which they can influence project decisions?
3. Does the person have an impact on project resources such as technical tools, personnel, or academic funding?
4. Does the person possess specialized skills or technical capabilities required by the project?
5. Does the person potentially benefit from the project or are they able to resist the transition to a digital booking system?

STAKEHOLDER ANALYSIS

Atasha
Frances
Gayle Doria



Pet Owner



Service
Provider



Team Lead/
Release Manager



Project
Manager



Lead
Developer



Lead Quality
Assurance



Dev Team



Marketing &
Sales Staff



Project
Adviser



Project
Co-Adviser



Competitors

STAKEHOLDER MANAGEMENT STRATEGY


Atasha
Frances
Gayle Doria



Key	Organization	Name	Power (1-5)	Interest (1-5)
A	Management Team	Lalainne Andaya	5	5
B	Management Team	Feliz Angelica Salting	5	5
C	Development Team	Atasha Frances Gayle Doria	4	5
D	Testing Team	Michelle Reina Pineda	4	5
E	Asia Pacific College Faculty	Mr. Gonzalo Gumogda	4	4
F	Asia Pacific College Faculty	Mr. Gil Ballesca	3	4
G	Users	Service Providers	3	3
H	Users	Pet Owners	3	3
I	External	Competitors	1	2

STAKEHOLDER MANAGEMENT STRATEGY

Atasha
Frances
Gayle Doria

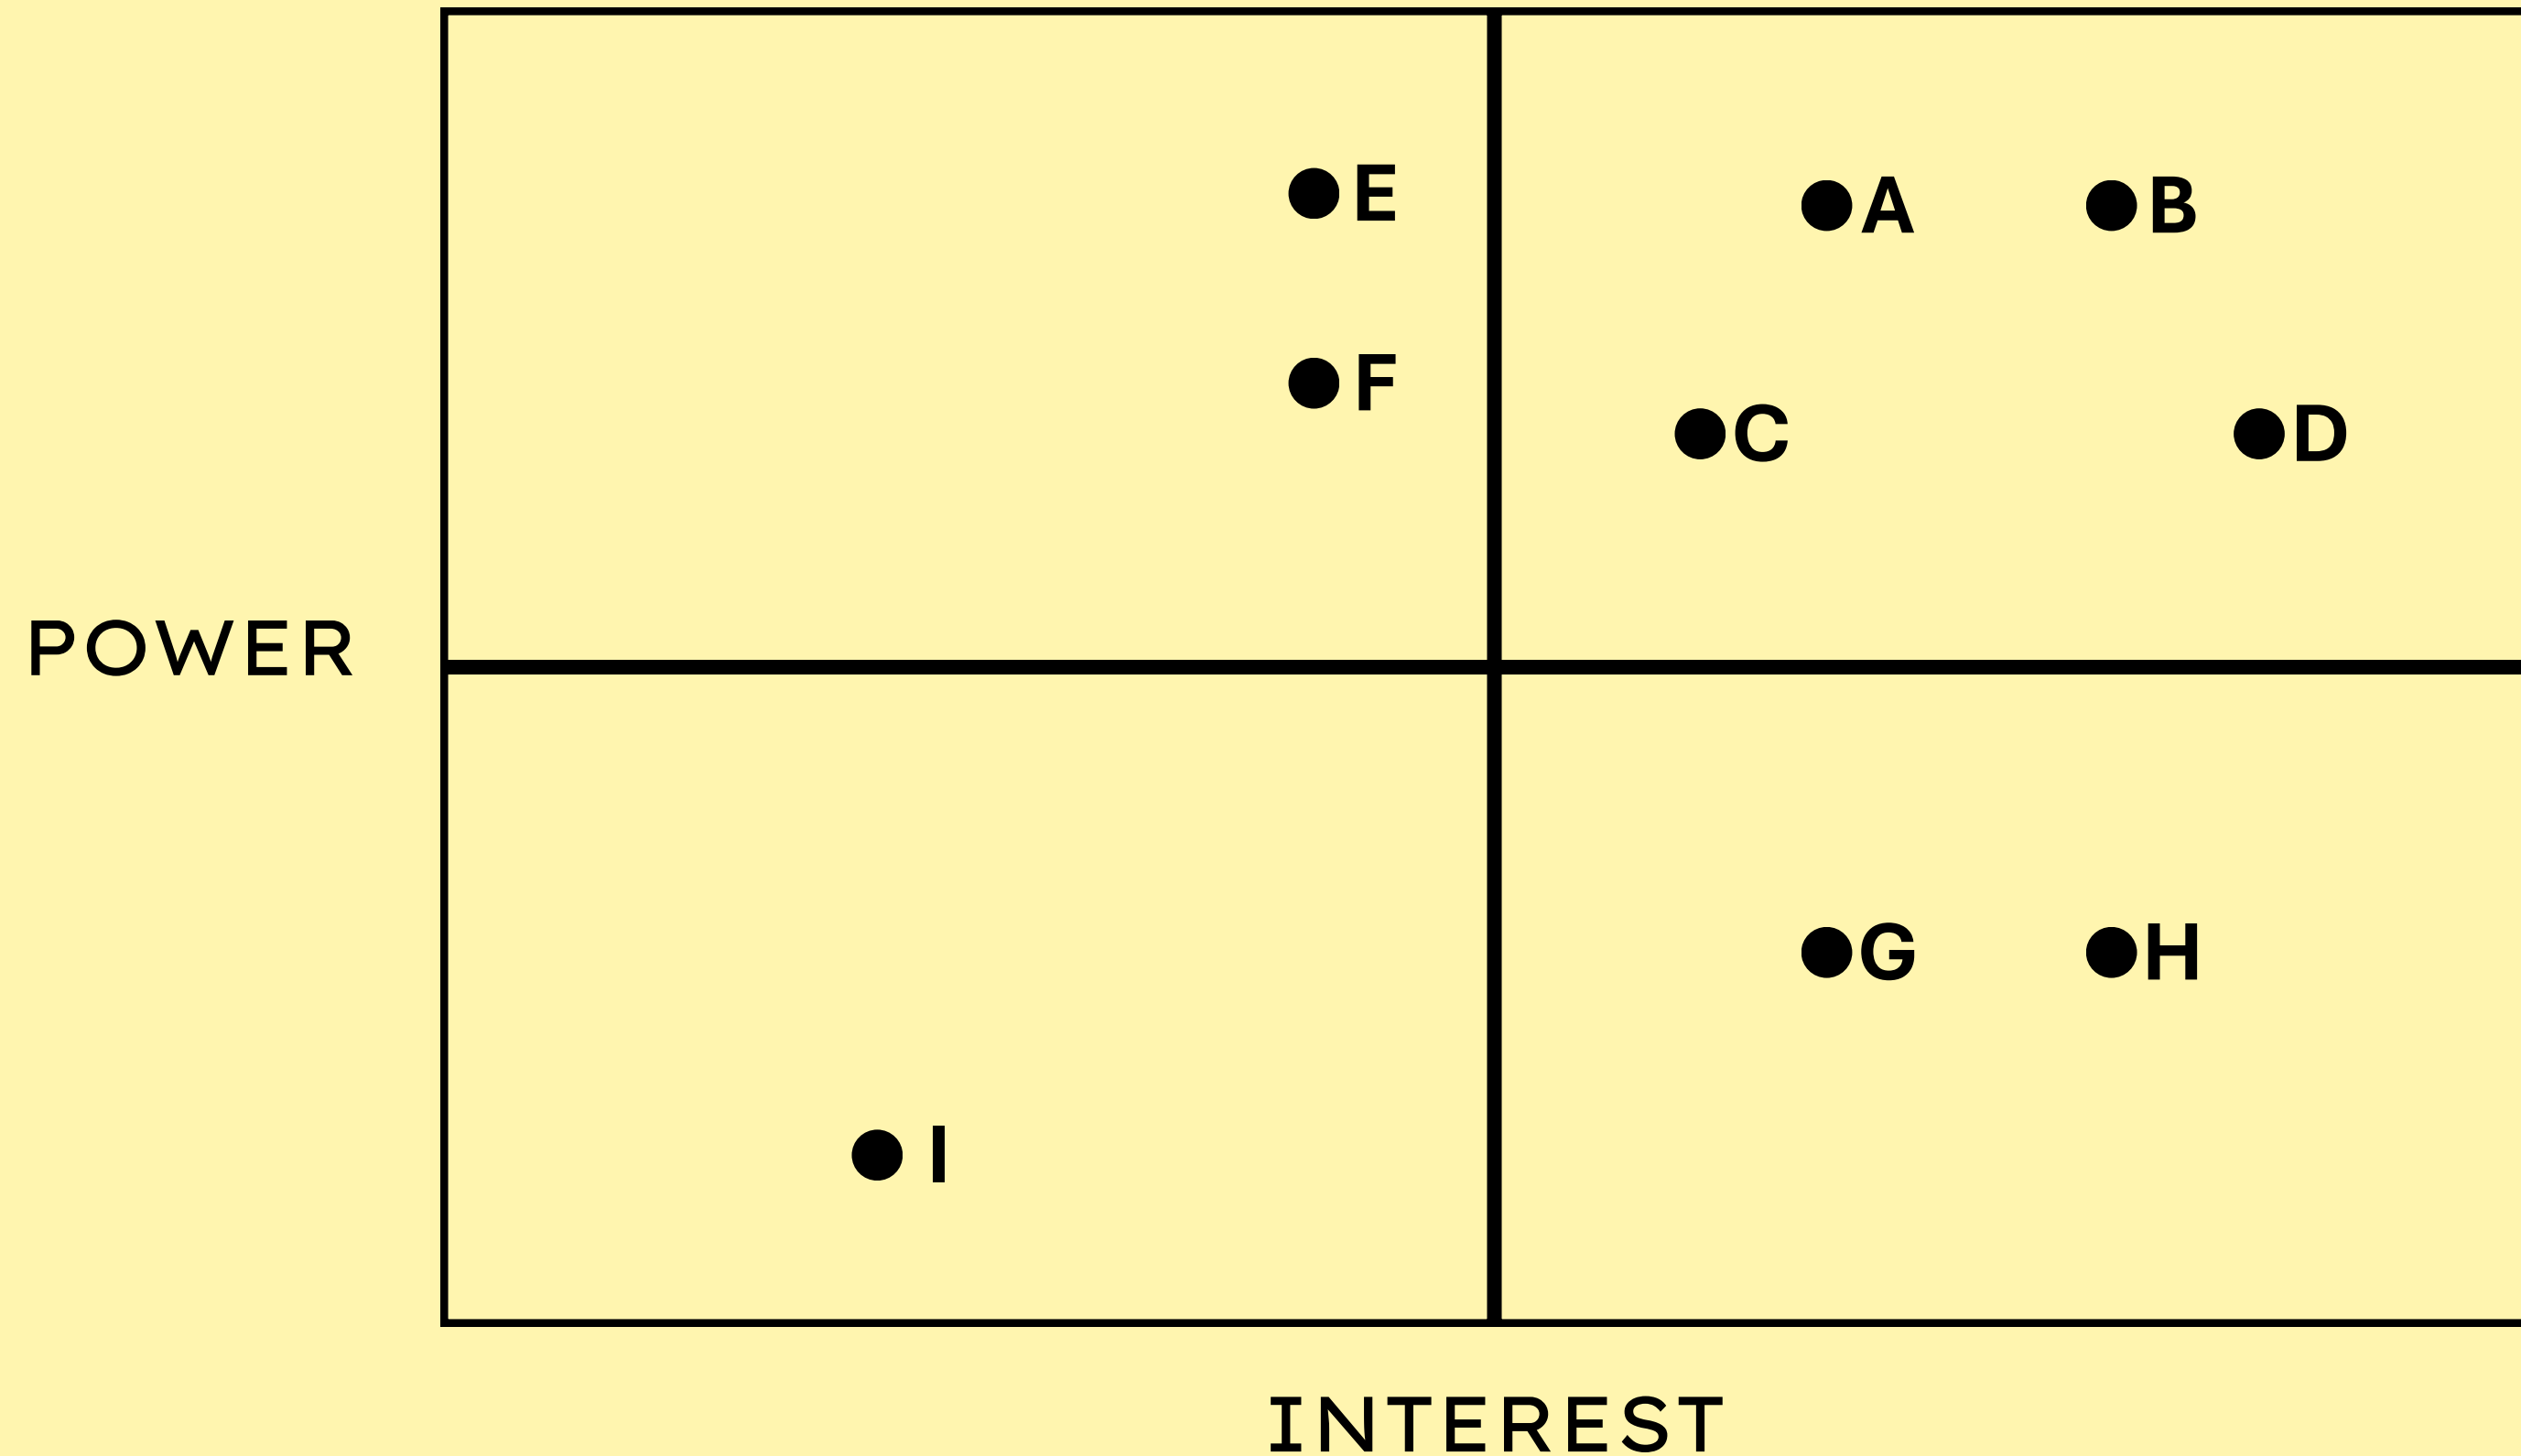

STATEMENT OF WORK

Lalainne
Andaya



BACKGROUND OF PROJECT

WORK REQUIREMENTS

SCOPE OF PROJECT

SCHEDULE

PERIOD OF PERFORMANCE

ACCEPTANCE CRITERIA

PLACE OF PERFORMANCE

OTHER REQUIREMENTS

2.0 PLANNING PHASE

COMMUNICATION MANAGEMENT

Lalaine
Andaya



COMMUNICATION APPROACH

Team communication is centered around transparency and real-time updates via OpenProject and Daily Stand-Ups

COMMUNICATION METHODS

- OpenProject for Task and Budget Tracking
- GitHub for Version Control and Code Review
- Teams Channel and Group Chats for daily sync and deliverables
- Microsoft SharePoint for deliverables
- Google Meet/Zoom for meetings with External Stakeholders

COMMUNICATION MATRIX

Lalainne
Andaya



Communication Type	Objective of Communication	Medium	Frequency	Audience	Owner	Deliverables	Format
Kickoff Meeting	Re-align the team on objectives, schedule, and new requirements.	- Face to Face - Online meeting	Once	- Project Team - Project Adviser	Project Manager	- Agenda - Meeting Minutes	Soft copy archived on PROJMAN team channel
Sprint Planning	Define sprint goals, review product backlog, and assign OpenProject work packages.	Online meeting	Once during the start of each Sprint	Project Team	- Project Manager - Scrum Master	- Sprint Backlpg - Updated Sprint Board	OpenProject Dashboard
Daily Stand-Up	Quick syn to discuss what was done yesterday, what will be done today, and identify blockers.	- Online meeting - Brief face to face	Minimum of 2 meetings a week for 15 minutes	Project Team	- Project Manager - Scrum Master	- Daily Status Update - Identified Blockers	OpenProject Forum

COMMUNICATION MATRIX

Lalaine
Andaya



Sprint Retrospective	Review what went well during the sprint, identify what didn't, and identify action items to improve next Sprint.	Online meeting	Once during the end of each Sprint	Project Team	- Project Manager - Scrum Master	- Retrospective Notes - List of Action Items	Soft copy archived on PROJMAN team channel
Adviser Status Consultations	Report on project milestones and receive academic guidance.	- Face to face - Online meeting	Once per week	- Project Team - Project Adviser	Project Manager	- Live Demo - Documentation - Meeting Notes	Soft copy on private channel and PROJMAN team channel
Defense Presentations	Formally present completed project milestones for academic grading and feedback.	Face to face presentation	Per academic milestone	- Steering Committee - Project Adviser	Project Team	- Slide Deck - Live Demo - System Documentation	Soft copy on private channel and PROJMAN team channel

SCOPE MANAGEMENT

Feliz
Angelica
Salting



DEFINING AND MANAGING THE SCOPE

- Features were defined through quantitative surveys (43 Makati pet owners) and qualitative interviews with local shop owners.
- The project uses a change request process to prevent "scope creep."

CORE PLATFORM FEATURES

- Calendar-based scheduling and service directory.
- AI Booking Assistant.
- Business analytics dashboard for service providers.

SCOPE MANAGEMENT

Feliz
Angelica
Salting



OUT OF SCOPE AND CONSTRAINTS

- The platform will not accommodate veterinary care, pet insurance, or pet transportation services.
- Budget is capped at ₱675, 332 (using open-source and free-tier solutions)
- Timeline is bound by the academic calendar (April 2026 - October 2026)
- At least one local grooming shop will fully onboard during the first launch.



SCOPE MANAGEMENT

Feliz
Angelica
Salting



PRODUCT ACCEPTANCE CRITERIA

- Unit Testing: 100% of unit test cases must pass with zero critical/major bugs.
- Integration Testing: Key modules (registration, AI, booking flow, dashboard) must communicate seamlessly.
- User Acceptance Testing (UAT): The system must be proven stable and validated by actual stakeholders in a real-world environment.



WORK BREAKDOWN STRUCTURE

Feliz
Angelica
Salting



SCHEDULE MANAGEMENT

Feliz
Angelica
Salting



SCHEDULE MANAGEMENT APPROACH

- The project utilizes a sprint-based approach, mapping WBS deliverables directly to deployment cycles.
- Task priority is dictated by technical dependencies
- Durations factor in known technical constraints, such as API webhook testing and Gemini 2.5 Flash AI rate limits.

SCHEDULE TRACKING

- Schedule progress is reviewed every two weeks, aligned with Agile sprint reviews.
- The Project Team holds standups to track actual start/finish dates and completion percentages.
- The Project Team is responsible for immediately communicating technical blockers to prevent delays.

SCHEDULE MANAGEMENT

Feliz
Angelica
Salting



SCHEDULE CHANGE THRESHOLDS

- Any change that increases or decreases an individual work package's duration by 10% or more requires a formal change request.
- Any estimate to push a major release milestone past its baseline date by more than 3 business days must be escalated.

SCOPE-DRIVEN SCHEDULE CHANGES

- Schedule progress is reviewed every two weeks, aligned with Agile sprint reviews.
- The Project Team holds standups to track actual start/finish dates and completion percentages.
- The Project Team is responsible for immediately communicating technical blockers to prevent delays.

QUALITY MANAGEMENT

Michelle
Reina
Pineda



Quality Assurance

Process Action	Acceptable Process Standards	Process Phase	Assessment Interval
Code Review	< 5 "Major" bugs found per module	Development	Per Feature/Sprint
API Integration	< 200ms response time from <u>Supabase</u>	Integration	Weekly or per run
UAT Sessions	> 90% positive "Ease of Use" rating	Testing Phase	Per UAT session

QUALITY MANAGEMENT

Michelle
Reina
Pineda



Quality Control

Product	Performance Standards	Quality Assessment Activities	Assessment Intervals
Booking Engine	100% data accuracy in <u>Supabase</u>	Automated Unit Testing	Per code commit
Frontend UI	100% Responsive on iOS/Android/Web	Cross-browser testing	Per produced module
Security	SSL Encryption & Secure Auth	Penetration testing	Pre-deployment

COST MANAGEMENT



BUDGET FOR SPRINT 2				
Category	Item	Unit Cost in PHP	Duration	Total in PHP
Labor	Project Manager	500 /hour	20 days	20000
	Developers	500 /hour	20 days	20000
	Release Manager	500 /hour	20 days	20000
	Quality Assurance	500 /hour	20 days	20000
Others	Co-Working Space	100 /hour	15 hours	1,500
	Contingency Reserve	10% of subtotal	20 days	8,150
SUBTOTAL				81500
TOTAL BUDGET FOR SPRINT 2				89650

- ASSUMPTIONS/
REQUIREMENTS:
- 10 Hours allocated per week
 - 40 Hours allocated per month
 - ₱500 Rate per hour for all members
 - 15 Units of Co-Working Space

AY 25-26 TERM 3 SPRINT 2

Added by Lalainne Andaya about 24 hours ago. Updated 44 minutes ago.

BUDGET DETAILS

Cost type

Budget

Fixed date

03/30/2026

Spent (ratio)

42%

Description

TOTALS

Base amount

PHP 0.00

Planned unit costs

PHP 9,650.00

Planned labor costs

PHP 80,000.00

Planned

PHP 89,650.00

Spent

-PHP 37,965.00

Available

PHP 51,685.00

UNITS

MEASURING PROJECT COST

Lalainne
Andaya



COSTS FOR SPRINT 2

Start Date End Date
3/30/2026 4/20/2026

PLANNED VALUE	
Number of Days	21
Sprint Budget	89,650
Reporting Date	4/7/2026
Planned % by Reporting Date	38%
	0.38
Calculation	0.38 x 89,650
PLANNED VALUE	34,067.00

EARNED VALUE	
Number of Days	21
Sprint Budget	89,650
Reporting Date	4/7/2026
Earned % by Reporting Date	100
	1.00
Calculation	100 x 89,650
EARNED VALUE	89,650.00

ACTUAL COST	
Number of Days	21
Sprint Budget	89,650
Reporting Date	4/7/2026
Total Spent	39065.00
ACTUAL COST	39,065.00

Formulas:

$$CV = EV - AC$$

$$SV = EV - PV$$

$$CPI = EV / AC$$

$$SPI = EV / PV$$

COST PERFORMANCE SUMMARY		
Cost Variance	50,585.00	Under Budget
Schedule Variance	55,583.00	Ahead of Schedule
Cost Performance Index	2.295	Good Cost Efficiency
Schedule Performance Index	2.631578947	Efficient

HUMAN RESOURCE

Michelle
Reina
Pineda



Key Project Roles

- Project Manager (PM)
 - Lead Developer (LD)
- QA Tester
 - Release Manager (RM)

Project Organization (RACI)

	Project Manager	Developers	QA Tester	Release Manager
Requirements Gathering	A	R	C	I
Database & Schema Design	A	R	I	C
Frontend & Backend Coding	I	R/A	C	I
Software & Unit Testing	A	C	R	I
User Acceptance Testing (UAT)	A	I	R	C
Environment Preparation	A	C	I	R
Final Implementation/Release	A	C	I	R

Key:

R – Responsible for completing the work


A – Accountable for ensuring task completion/sign off

C – Consulted before any decisions are made

I – Informed of when an action/decision has been made

HUMAN RESOURCE

Michelle
Reina
Pineda

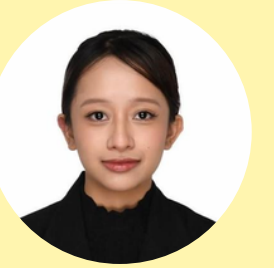


Staffing Management

Acquisition: Internal student

Timeline: Four-month duration (March to June); all roles perform 40 hours of work per month.

Training: No formal training scheduled; team will utilize free online resources

Performance: PM will evaluate based on successful "sprints" and code quality.

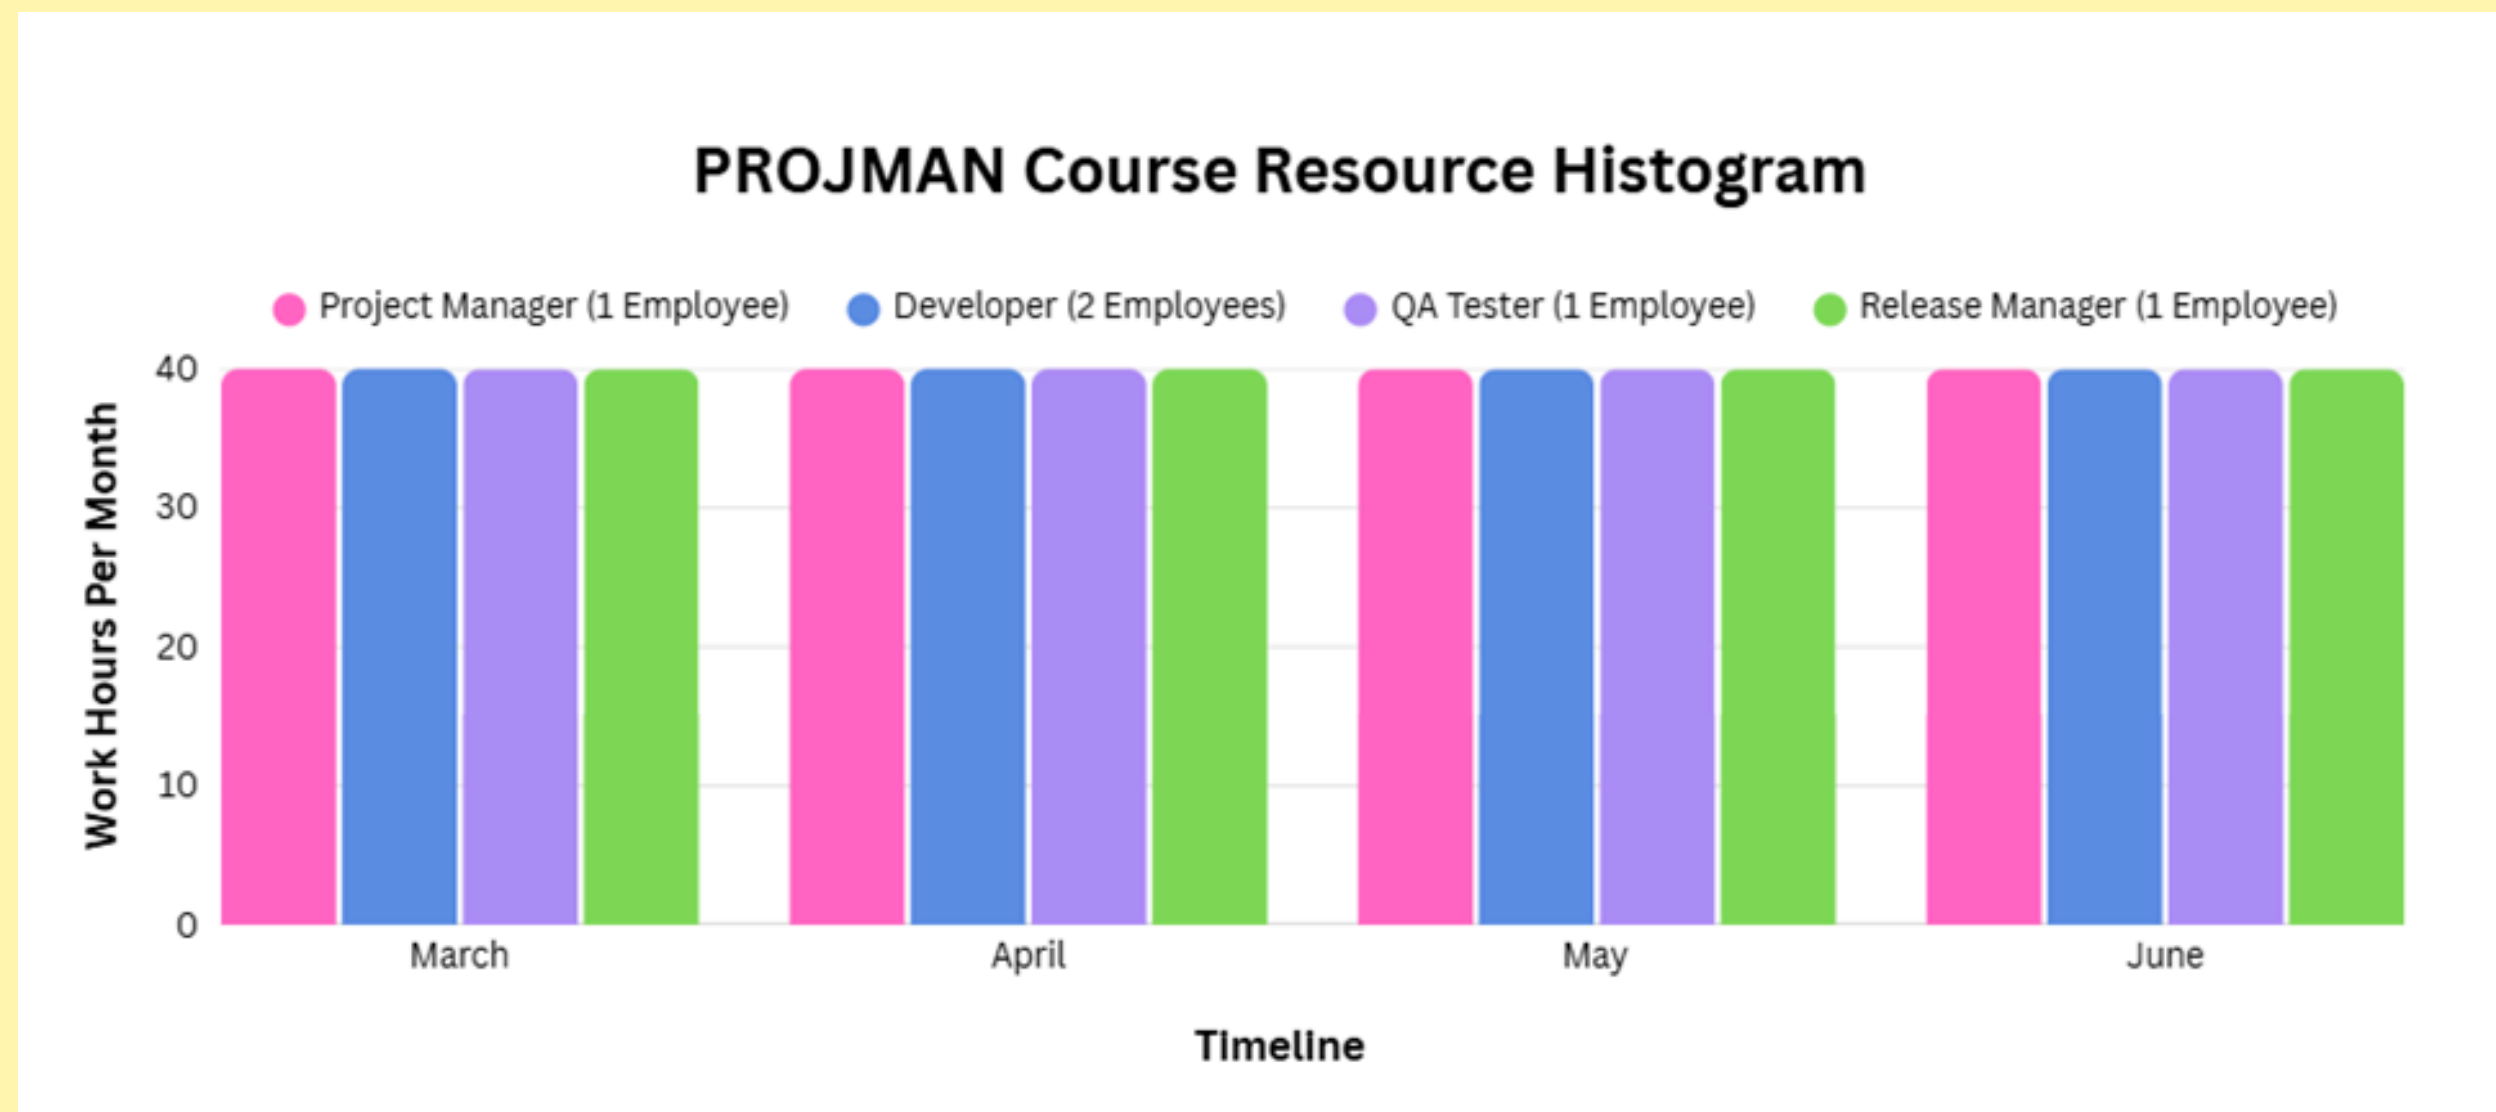

HUMAN RESOURCE

Michelle
Reina
Pineda




Recognition and Rewards

- Goal: Maintain team motivation during furlink's development.
- Milestone Event: A "Launch Party" will be held for the team upon the successful first booking on furlink.
- Recognition: Performance feedback provided directly during project status meetings.



AGILE TEAM VALUES

Michelle
Reina
Pineda

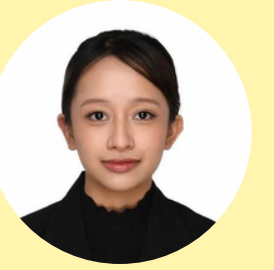

Shared Values



Communication



Ambitious



Resilient



Reliability

AGILE TEAM CHARTER

Lalainne
Andaya



Rules of Behavior

Contribution

- **Active Engagement:** Every team member must commit to communicating clearly and actively, ensuring everyone shares the necessary updates required for project progress.
- **Feedback Integration:** Everyone must actively respond to feedback given by the team, project advisers, or the steering committee.
- **Active Contribution:** Every team member must contribute to the charter and sprint planning to maintain a sense of ownership.
- **Proactive Innovation:** Every team member must take the initiative to bring realistic new ideas that push the boundaries of the platform's current capabilities.

Transparency

- All blockers must be reported during Daily Stand-ups to ensure the schedule remains on track.

Accountability

- **Quality and Assurance:** Every team member must provide results that exceed expectations, ensuring the work is accurate to minimize the need for re-work.
- **Active Accountability:** Team members are responsible for moving their own OpenProject work packages to Closed after the work has been tested and verified

Professionalism

- All internal and external communication must follow the standards defined in the project's Communication Plan

Team Communication

As an Agile team, we prioritize interpersonal communication over formalized documentation.

- We will conduct daily stand-up meetings via the PROJMAN group channel to discuss progress and immediate blockers.
- We will make every effort to attend all scheduled meetings in person or online, in exception for members who feel unwell/sick.
- The team will update tasks on OpenProject.
- Meeting minutes must be provided within 24 hours after the meeting.
- If a meeting is cancelled or additional meetings are required, the project team lead will send out notification as soon as possible.
- All team members are expected to be on time for all meetings.

SYSTEM DESIGN DOCUMENT

Atasha
Frances
Gayle Doria



Design Constraints

- Hardware and Technology Constraints
 - Constant Internet Requirement
 - Serverless Cold Start Delays
 - AI Rate Limiting
- Software and System Integration
 - Payment Webhook Dependency
 - Role-Based Access Complexity
 - AI Context Window Dependency
- Standards and Legal Rules
 - Data Privacy Compliance
 - Payment Handover
 - Pet Care Operational Workflows
 - Audit Accountability

SYSTEM DESIGN DOCUMENT

Atasha
Frances
Gayle Doria



SYSTEM ARCHITECTURE



User Device

SYSTEM DESIGN DOCUMENT

Atasha
Frances
Gayle Doria



SYSTEM ARCHITECTURE

Frontend



Backend

- Supabase Auth with JWT
- Supabase Row Level Security
- Supase Edge Functions
- Gmail SMTP

SYSTEM DESIGN DOCUMENT

Atasha
Frances
Gayle Doria



SYSTEM ARCHITECTURE


Payments



Version Control
and Collaboration



Artificial Intelligence



SYSTEM DESIGN DOCUMENT

Atasha
Frances
Gayle Doria



SOFTWARE MODULES

- Authentication and Access Control Module
- User Profile Management Module
- Pet Profile Module
- Service Provider Onboarding Module
- Platform Admin Oversight and Moderation Module
- Transaction and Payment Module
- Transaction and Payment Module
- Provider Operations Module
- Cancellation and Rescheduling Module
- Business Intelligence Dashboard Module
- AI Booking Assistant Module
- Discovery and Filtering Module

SYSTEM DESIGN DOCUMENT

Atasha
Frances
Gayle Doria



DATABASE DESIGN

- Cloud Infrastructure
- Built-in Security
- Modular Design
- Automated Logic
- AI Integration

SECURITY AND INTEGRITY CONTROLS

- Multi-tiered Authentication
- Database-Level Security
- Payment & AI Sandbox
- Data Privacy & Storage
- Backend Integrity

INDIVIDUAL CONTRIBUTION



Lalainne Andaya

Created the following documents:

- 01 Initiation 08 Statement of Work
- 02 Project Planning 01 Communication Management Plan
- 02 Project Planning 04 Scope Management Plan
- 02 Project Planning 13 Cost Management Plan
- Agile Team Charter

INDIVIDUAL CONTRIBUTION



Atasha Frances
Gayle Doria

Created the following documents:

- 01 Initiation 07 Stakeholder Management Strategy
- 01 Initiation 07B Stakeholder Analysis
- 07 Project Documents 04 System Design Document

INDIVIDUAL CONTRIBUTION



Michelle Reina
Pineda

Created the following documents:

- 01 Initiation 05 Project Brief
- 02 Project Planning 10 Quality Management Plan
- 02 Project Planning 16 Human Resource Plan
- Agile Team Values

INDIVIDUAL CONTRIBUTION



Feliz Angelica
Salting

Created the following documents:

- 01 Initiation 01 Project Charter
- 01 Initiation 03 Business Case
- 02 Project Planning 05 Work Breakdown Structure
- 02 Project Planning 06



ANDAYA, DORIA, PINEDA, SALTING
