

Communication Management Plan

furlink

Asia Pacific College

Humabon Place, Magallanes Village

Makati City, Metro Manila, 1232

April 2026

Table of Contents

Introduction	2
Communications Management Approach	2
Communications Management Constraints	2
Stakeholder Communications Requirements	3
Roles	3
Project Sponsor	3
Program Manager / Project Adviser	4
Key Stakeholders	4
Change Control Board	4
Project Manager	5
Project Team	5
Steering Committee	5
Technical Lead	5
Project Team Directory	6
Communication Methods and Technologies	7
Communication Matrix	8
Communication Flowchart	10
Guidelines for Meetings	10
Meeting Agenda	10
Meeting Minutes	11
Action Items	11
Meeting Chair Person	11
Secretary	11
Parking Lot	11
Communication Standards	11
Communication Escalation Process	12
Glossary of Communication Terminology	13
Sponsor Acceptance	14

Introduction

This Communications Management Plan sets the communications framework for this project. It will serve as a guide for communications throughout the life of the project and will be updated as communication needs change. This plan identifies and defines the roles of people involved in this project. It also includes a communications matrix which maps the communication requirements of this project. An in-depth guide for conducting meetings details both the communications rules and how the meetings will be conducted, ensuring successful meetings. A project team directory is included to provide contact information for all stakeholders directly involved in the project.

Communications Management Approach

The Project Manager will take a proactive role in ensuring effective communications on this project. The communications requirements are documented in the Communications Matrix presented in this document. The Communications Matrix will be used as the guide for what information to communicate, who is to do communication, when to communicate, and to whom to communicate.

As with most project plans, updates or changes may be required as the project progresses or changes are approved. Changes or updates may be required due to changes in personnel, scope, budget, or other reasons. Additionally, updates may be required as the project matures, and additional requirements are needed. The project manager is responsible for managing all proposed and approved changes to the communications management plan. Once the change is approved, the project manager will update the plan and supporting documentation and will distribute the updates to the project team and all stakeholders. This methodology is consistent with the project's Change Management Plan and ensures that all project stakeholders remain aware and informed of any changes to communications management.

Communications Management Constraints

All project communication activities will occur within the project's approved budget, schedule, and resource allocations. The project manager is responsible for ensuring that communication activities are performed by the project team without external resources,

which will result in exceeding the authorized budget. Communication activities will occur in accordance with the frequencies detailed in the Communication Matrix in order to ensure the project adheres to schedule constraints. Any deviation of these timelines may result in excessive costs or schedule delays and must be approved by the project sponsor.

Everyone part of the project, must first obtain the approval of all the other members to authorize the distribution of confidential information. The project manager is responsible for ensuring that approval is requested and obtained prior to the distribution of any confidential information and materials regarding this project.

Stakeholder Communications Requirements

As part of identifying all project stakeholders, the project manager will communicate with each stakeholder in order to determine their preferred frequency and method of communication. Standard project communications will occur in accordance with the Communication Matrix; however, depending on the identified stakeholder communication requirements, individual communication is acceptable and within the constraints outlined for this project.

In addition to identifying communication preferences, stakeholder communication requirements must identify the project's communication channels and ensure that stakeholders have access to these channels. If project information is communicated via secure means or through internal resources, all stakeholders, except for Service Providers, must have the necessary access to receive project communications.

Once all stakeholders have been identified and communication requirements are established, the project team will maintain this information in the project's Stakeholder Register and use this, along with the project communication matrix as the basis for all communications.

Roles

Project Sponsor

The project sponsors for *furlink* consist of the project team members and their immediate family members who provide the foundational financial backing and logistical support for the project. As the primary funders, they are ultimately invested in its success.

Communications to the sponsors should be presented in a summary format detailing project milestones, budget health, and major achievements, unless more detailed financial or scheduling updates are requested.

Project Adviser

In the context of this academic project, the Project Adviser fulfills the role of a program manager overseeing the project within the School of Computing and Information Technologies. The Project Adviser is responsible for ensuring that the project meets academic standards, course requirements, and timelines. They require more detailed, frequent communications than Project Sponsors, including progress reports, technical blockers, and updates.

Key Stakeholders

While many individuals are impacted by *furlink*, the Key Stakeholders for this specific communication plan include the peer reviewers, and early-adopter grooming service providers. These are the stakeholders who require targeted communication regarding beta testing schedules and deployment impacts, but are not involved in the day-to-day execution.

Change Control Board

For the *furlink* capstone initiative, the Change Control Board (CCB) functions as the definitive approval authority for all proposed changes to the project's scope, timeline, budget, or multi-cloud infrastructure. Chaired by the Project Adviser and Co-Adviser, and including the Project Manager and Lead Developer, this collaborative group rigorously evaluates technical specifications and requested modifications against strict academic deadlines. The CCB ensures that any authorized changes are absolutely essential to delivering the core MVP and do not introduce scope creep that could jeopardize the final solution release.

Project Manager

Responsible for the overall success of the Project. The PM must authorize and approve all project expenditures. The PM is also responsible for approving that work activities meet established acceptability criteria and fall within acceptable variances. The PM will be responsible for reporting project status in accordance with the communications

management plan. The PM will evaluate the performance of all project team members. The PM must possess the following skills: leadership/management, budgeting, scheduling, and effective communication.

Lead Full-Stack Developer

Accountability for the end-to-end technical architecture, code security, and final deployment of the furlink web application. The LD holds the authority to make critical decisions regarding the core tech stack, external library integrations, database schema modifications, and deployment workflows. Primary responsibilities include designing the system architecture, setting up the Supabase database infrastructure, configuring third-party APIs (Gemini AI and PayMongo), and overseeing the repository's main code branch. This role requires advanced technical competency in Vite, Node.js, and PostgreSQL, along with strong leadership skills to guide code freezes, conduct code reviews, and cross-train team members on database conflict resolution.

Full-Stack Developer

Responsible for the core feature development, implementation, and maintenance of both the user interface and backend application logic. The FD has the authority to implement design patterns, write specific API queries, and construct reusable components within the established architectural guidelines. Primary responsibilities include translating user stories into responsive UI components using Vite/CSS, managing Supabase backend data queries, handling CRUD operations for provider listings, and building real-time dashboard analytics. This role requires technical proficiency in JavaScript, CSS, and database manipulation, with a focus on ensuring the platform functions seamlessly across various mobile viewports and browser environments.

Quality Assurance Tester

The QA Tester focuses on ensuring the reliability and user-friendliness of the platform by developing comprehensive test plans that cover both manual functional testing and automated regression suites. This role holds the authority to flag critical bugs that could delay a release, ensuring that the software is thoroughly validated before it reaches the end user. Responsibilities include documenting all identified issues, verifying technical fixes, and facilitating User Acceptance Testing (UAT) sessions with actual pet service providers to measure the platform's ease of use. Success in this role requires strong analytical skills and

a deep understanding of the Software Testing Life Cycle (STLC) to prevent data errors or UI failures.

Project Team Directory

Role	Name	Title	Organization/ Department	Email
Project Sponsor Representative	Manuel R. Doria	Sponsor Representative	LogiTeh	manueldoria14@yahoo.com
Project Adviser	G. Gumogda	Project Adviser	APC-SOCIT	gonzalog@apc.edu.ph
Project Manager	Lalaine Andaya	Project Manager	LogiTeh	lcandaya2@student.apc.edu.ph
Project Stakeholders	See Stakeholder Register	See Stakeholder Register	See Stakeholder Register	See Stakeholder Register
Lead Full-Stack Developer	Atasha Frances Gayle Doria	Lead Developer	LogiTeh	asdoria@student.apc.edu.ph
Full-Stack Developer	Feliz Angelica Salting	Release Manager / Team Lead	LogiTeh	fpsalting@student.apc.edu.ph
Quality Assurance	Michelle Reina Pineda	QA Lead	LogiTeh	mbpineda@student.apc.edu.ph

Communication Methods and Technologies

The LogiTeh project team will determine, in accordance with the Asia Pacific College School of Computing and Information Technologies (APC-SOCIT) guidelines, the communication methods and technologies based on several factors. These include stakeholder communication requirements, available technologies (internal and external), and academic organizational standards.

LogiTech utilizes an OpenProject Team Site as the primary project management information system. All project team members use this platform to provide updates, track sprint progress, and manage the product backlog. This platform enables the Project Manager and the Project Adviser to monitor project data, activities, and task completion at any point in time.

For the Steering Committee, Defense Panel, and formal document submissions, the team utilizes a dedicated Project SharePoint site. The Project Manager is responsible for ensuring all formal project communications, final deliverables, and documentation are uploaded and organized within this SharePoint platform.

For external stakeholders (such as pilot grooming service providers) who do not have access to OpenProject or the academic SharePoint, communication will be conducted via direct email and virtual meetings through Google Meet.

All technical project communication regarding software development and version control, will be maintained and archived on both the GitHub APC-SOCIT project repository and a public GitHub repository of the project.

Communication Matrix


The following table identified the communications requirements for this project

Communication Type	Objective of Communication	Medium	Frequency	Audience	Owner	Deliverables	Format
Kickoff Meeting	Re-align the team on objectives, schedule, and new requirements.	- Face to Face - Online meeting	Once	- Project Team - Project Adviser	Project Manager	- Agenda - Meeting Minutes	Soft copy archived on PROJMAN team channel
Sprint Planning	Define sprint goals, review product backlog, and assign OpenProject work packages.	Online meeting	Once during the start of each Sprint	Project Team	- Project Manager - Scrum Master	- Sprint Backlpg - Updated Sprint Board	OpenProject Dashboard
Daily Stand-Up	Quick sync to discuss what was done yesterday, what will be done today, and identify blockers.	- Online meeting - Brief face to face	Minimum of 2 meetings a week for 15 minutes	Project Team	- Project Manager - Scrum Master	- Daily Status Update - Identified Blockers	Meeting recording in Microsoft PROJMAN team channel Verbal Updates

Sprint Retrospective	Review what went well during the sprint, identify what didn't, and identify action items to improve next Sprint.	• Online meeting	Once during the end of each Sprint	• Project Team	• Project Manager • Scrum Master	• Retrospective Notes • List of Action Items	Soft copy archived on PROJMAN team channel
Adviser Consultations	Report on project milestones and receive academic guidance.	• Face to face • Online meeting	Once per week	• Project Team • Project Adviser	Project Manager	• Live Demo • Documentation • Meeting Notes	Soft copy of meeting minutes on private channel and PROJMAN team channel
Platform Onboarding and Training	Guide the service provider through using the furlink platform.	• Online meeting • Face to face	Once	• Initial Onboarded Service Providers	Project Manager	• User Manual Guide	PDF Manual, soft copy archived in private team channel and SharePoint

Communication Flowchart

The communication flowchart below was created to aid in project communication. This flowchart provides a framework for the project team to follow for this project. However, there may be occasions or situations which fall outside of the communication flowchart where additional clarification is necessary. In these situations, the Project Manager is responsible for discussing communication with the Project Sponsor and making a determination on how to proceed.

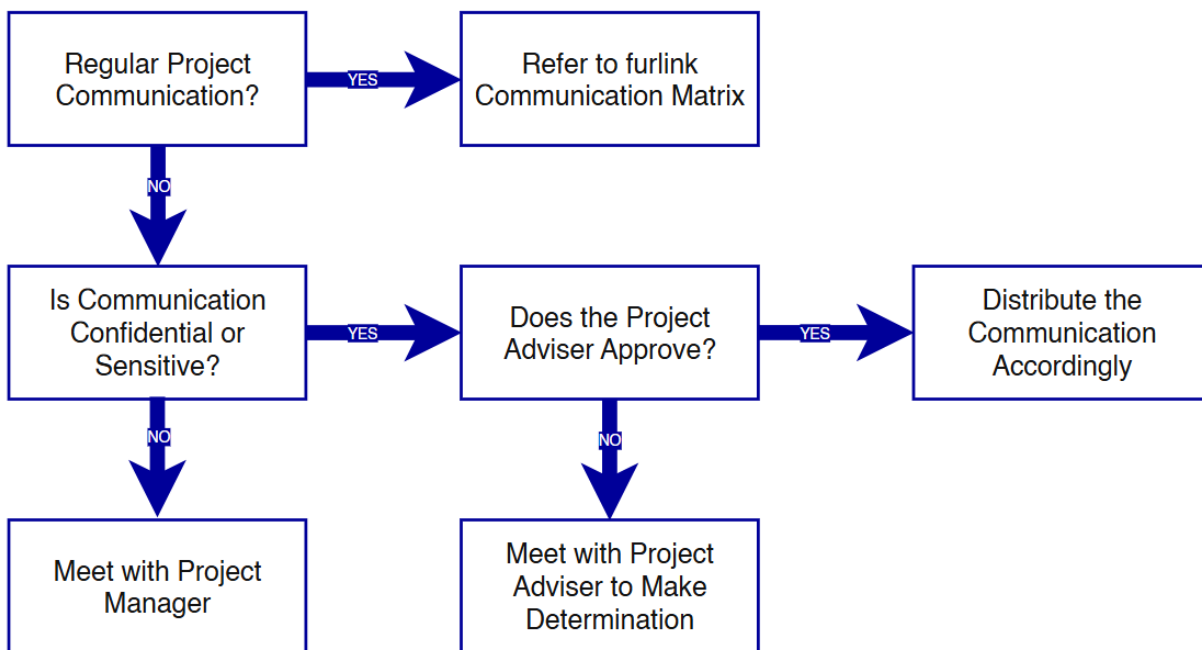

Guidelines for Meetings

Meeting Agenda

For meetings that are not the Sprint Planning, Daily Stand-Ups, and Sprint Retrospective, the meeting agendas will be distributed upon sending a calendar meeting request. The agenda should identify the main presented along with the maximum time for the meeting.

Meeting Minutes

Meeting minutes will be uploaded to the PROJMAN LogiTeh group channel within 2 business days following the meeting. Meeting minutes must follow the meeting minutes template uploaded in the group channel files and must contain action items.

Action Items

Action Items are recorded in the meeting minutes. Action items will include the action item along with who must do the action item. Meetings will start with a review of the status of all action items from previous meetings and end with a review of all action items.

Meeting Chairperson

The Chairperson is responsible for distributing the meeting agenda, facilitating the meeting and ensuring that the meeting minutes are readily available in the team's Team Channel. The Chairperson will ensure that the meeting starts and ends on time and that all presenters adhere to their allocated time frames.

Secretary

The Secretary is responsible for taking the minutes, and helping the facilitator adhere to the time limits set in the meeting agenda. The Secretary will let the presenter know when they are approaching the end of their allocated time.

Parking Lot

The Parking Lot is used by the facilitator to record and defer items which are not on the meeting agenda, however, it will be further discussed at a later time or through another forum. A parking lot record should identify an owner for the item as that person will be responsible for ensuring follow-up.

Communication Standards

For this project, the LogiTeh team will utilize standard Asia Pacific College (APC-SOCIT) formats and internal LogiTeh templates for all formal project communications. These communications, as detailed in the project’s communication matrix, include:

- **Kickoff and Panel Defense:** The project will utilize standard APC-SOCIT presentation templates. Formal meeting minutes and agendas will be drafted using LogiTeh document templates and archived on SharePoint and team channels.
- **Sprint Ceremonies:** The project team will utilize standard OpenProject ticket formats to track tasks. Daily stand-up updates will follow a standardized “Yesterday, Today, Blockers” reporting format in meetings and OpenProject Forum.
- **Adviser Status Consultation:** The team will use a standard Project Status Report to summarize milestone progress, budget health, and roadblocks prior to each meeting with the Project Adviser.

Informal project communication must remain professional and effective, but there is no template that must be used outside of the agreed-upon platforms.

Communication Escalation Process

Efficient and timely communication is key to successfully completing furlink by October 2026. Therefore, it is imperative that any disputes, conflicts, or discrepancies regarding project communications are resolved in a way that maintains the project schedule, ensures correct data distribution, and aligns with academic requirements.

To ensure the project stays on track, the LogiTeh team will use the following escalation model. This provides a clear hierarchy for resolving communication issues, defining priority levels, decision authorities, and required timeframes for resolution.

Priority Level	Definition	Decision Authority	Timeframe for Resolution
Priority 1: Critical	Major disputes or issues that affect the project’s viability, ethical compliance, or funding.	Project Adviser and Steering Committee	Addressed immediately, within 5 hours
Priority 2: High	Conflicts involving project scope changes, academic	Project Adviser	Within 3 to 5 business days

	grading and requirements, or external customer communication.		
Priority 3: Medium	Technical disputes regarding system architecture, GitHub merges, or API integration that may impact the sprint schedule.	Technical Lead and Project Manager	Within 48 hours
Priority 4: Low	Internal miscommunications regarding tasks, OpenProject tickets, or daily sprint goals and blockers.	Project Manager and Team Lead	Within 24 hours

** NOTE: Any communication including sensitive and/or confidential information will require escalation to Project Adviser for approval prior to external distribution.

Glossary of Communication Terminology

Term	Definition
Communication	The effective sending and receiving of information. Ideally, the information received should match the information sent. It is the responsibility of the sender to ensure this takes place.
Stakeholder	Individuals or groups involved in the project or whose interests may be affected by the project's execution or outcome.
Communications Management Plan	Portion of the overall Project Management Plan which details how project communications will be conducted, who will participate in communications, frequency of communications, and methods of communications.
Escalation	The process which details how conflicts and issues will be passed up the management chain for resolution as well as the timeframe to achieve resolution.

Sponsor Acceptance

Approved by the Project Sponsor:



Manuel R. Doria Jr.

Date: April 7, 2026

Project Sponsor Representative

