

Human Resource Plan

furlink

Humabon Place, Magallanes Village

Makati City, Metro Manila, 1232

April 2026

Table of Contents

1. Introduction3

2. Roles and Responsibilities.....3

3.Project Organizational Charts5

4. Staffing Management6

Sponsor Acceptance8

Introduction

Human resources management is a critical component of the furlink project. This plan serves as a tool to aid in the management of human resource activities from development through to User Acceptance Testing (UAT) and final deployment Roles and responsibilities of team members throughout the project

The furlink Human Resource Plan includes:

- Roles and Responsibilities: Clear definitions for team members.
- Project Organization Charts: Visualizing hierarchy and task assignments.
- Staffing management plan to include:
 - a. How resources will be acquired
 - b. Timeline for resources/skill sets
 - c. Training required to develop skills
 - d. How performance reviews will be conducted
 - e. Recognition and rewards system

The goal is to ensure the project has the necessary technical skills (React.js, Supabase, QA testing) and that team activities are effectively managed to meet the project's social impact goals.

Roles and Responsibilities

The roles and responsibilities for the Software Upgrade Project are essential to project success. All team members must clearly understand their roles and responsibilities in order to successfully perform their portion of the project. The following project team roles and responsibilities have been established:

Project Manager (PM), (1 position): Responsible for the overall success of the Project. The PM must authorize and approve all project expenditures. The PM is also responsible for approving that work activities meet established acceptability criteria and fall within acceptable variances. The PM will be responsible for reporting project status in accordance with the communications management plan. The PM will evaluate the performance of all

project team members. The PM must possess the following skills: leadership/management, budgeting, scheduling, and effective communication.

Lead Full-Stack Developer (LD), (1 position): Accountability for the end-to-end technical architecture, code security, and final deployment of the furlink web application. The LD holds the authority to make critical decisions regarding the core tech stack, external library integrations, database schema modifications, and deployment workflows. Primary responsibilities include designing the system architecture, setting up the Supabase database infrastructure, configuring third-party APIs (Gemini AI and PayMongo), and overseeing the repository's main code branch. This role requires advanced technical competency in Vite, Node.js, and PostgreSQL, along with strong leadership skills to guide code freezes, conduct code reviews, and cross-train team members on database conflict resolution.

Full-Stack Developer (FD), (1 position): Responsible for the core feature development, implementation, and maintenance of both the user interface and backend application logic. The FD has the authority to implement design patterns, write specific API queries, and construct reusable components within the established architectural guidelines. Primary responsibilities include translating user stories into responsive UI components using Vite/CSS, managing Supabase backend data queries, handling CRUD operations for provider listings, and building real-time dashboard analytics. This role requires technical proficiency in JavaScript, CSS, and database manipulation, with a focus on ensuring the platform functions seamlessly across various mobile viewports and browser environments.

QA Tester (QA): The QA Tester focuses on ensuring the reliability and user-friendliness of the platform by developing comprehensive test plans that cover both manual functional testing and automated regression suites. This role holds the authority to flag critical bugs that could delay a release, ensuring that the software is thoroughly validated before it reaches the end user. Responsibilities include documenting all identified issues, verifying technical fixes, and facilitating User Acceptance Testing (UAT) sessions with actual pet service providers to measure the platform's ease of use. Success in this role requires strong analytical skills and

a deep understanding of the Software Testing Life Cycle (STLC) to prevent data errors or UI failures.

Project Organizational Charts

The following RACI chart shows the relationship between project tasks and team members. Any proposed changes to project responsibilities must be reviewed and approved by the project manager. Changes will be proposed in accordance with the project's change control process. As changes are made, all project documents will be updated and redistributed accordingly.

Project Phase / Activity	Project Manager	Lead Full-Stack Dev	Full-Stack Dev	QA Tester
Requirements Gathering	R	A	C	C
Database & Schema Design	A	R	R	I
Frontend & Backend Coding	I	A	R	C
Software & Unit Testing	A	C	C	R
User Acceptance Testing (UAT)	A	I	I	R
Environment Preparation	A	R	C	I
Final Implementation / Release	A	R	C	I
Project Documentation	A	R	R	R

Key:

R – Responsible for completing the work

A – Accountable for ensuring task completion/sign off

C – Consulted before any decisions are made

I – Informed of when an action/decision has been made


Staffing Management

Staff Acquisition:

Project staff for furlink consists of internal student resources. The Project Manager identifies and assigns resources based on the technical requirements of the platform. All resources will work remotely or from the designated campus workspace.

Resource Calendars:

The PROJMAN Course will last for four months. All resources are required before the project begins. The resource histogram below illustrates that the Project Manager, Full- Stack Developers, and QA Tester will all perform work for a maximum of 40 hours per month from March to June.

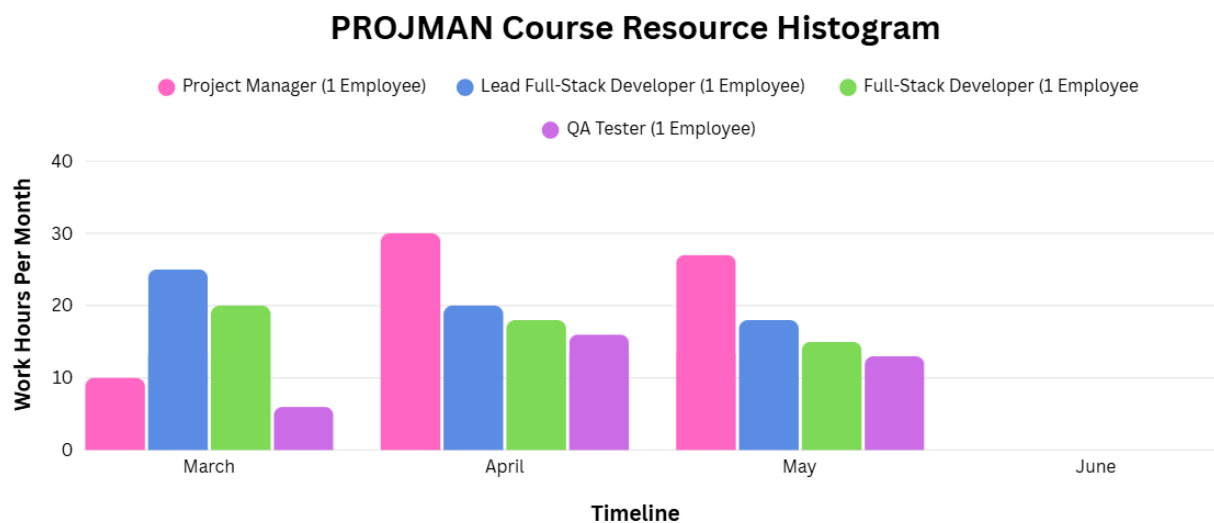

Performance Reviews:

The PM will evaluate team members based on the successful completion of "sprints" and the quality of code/documentation produced. Feedback will be provided during project status meetings.

Recognition and Rewards:

To maintain motivation throughout the development of the pet grooming platform:

- **Completion Event:** A "Launch Party" for the team upon the successful first booking on the platform.

Sponsor Acceptance

Approved by the Project Sponsor:



Manuel R. Doria Jr.

Project Sponsor Representative

Date: April 7, 2026
