

LogiTeh Sprint 2 Outputs

Contents

Sprint 2 Backlogs	2
Sprint Planning Output	3
Sprint Planning Meeting	3
Action Items	3
Openproject Board	4
Daily Standup Outputs	6
April 27, 2026, DSU	6
Forum	7
April 29, 2026, DSU	8
Forum	9
May 4, 2026 DSU	10
Forum	11
May 7, 2026 DSU	12
Backlog Refinement	14
OpenProject Board	14
Sprint Review	15
Burndown Chart	16
Sprint Retrospective	16
Sprint Retrospective Board	17

LogiTech Sprint 2 Outputs


Sprint 2 Backlogs

Term 3 Sprint 2 11 ^		04/25/2026 – 05/07/2026	129 points	...
::	USER STORY #6673 Closed	1.1.8 Create Feasibility study	7 points	...
::	USER STORY #6671 Closed	1.1.7 Create Business Model Canvas	6 points	...
::	USER STORY #6687 Closed	2.1.9 Create Requirements Management Plan	13 points	...
::	USER STORY #6683 Closed	2.1.8 Create Project Risk Management Plan	13 points	...
::	USER STORY #6688 Closed	2.1.10 Create Risk register	14 points	...
::	USER STORY #5487 New	5.1.1 Create transition out plan	15 points	...
::	USER STORY #6694 Closed	5.1.2 Create Project acceptance	10 points	...
::	USER STORY #6695 Closed	5.1.3 Create post project review	16 points	...
::	USER STORY #6696 Closed	5.1.4 Create lessons learned	7 points	...
::	USER STORY #6692 Closed	4.1.1 Create Project monitoring and controlling project status report	13 points	...
::	USER STORY #6690 Closed	2.1.12 Create change management plan	15 points	...

LogiTeh Sprint 2 Outputs

Sprint Planning Output

Sprint Planning Meeting

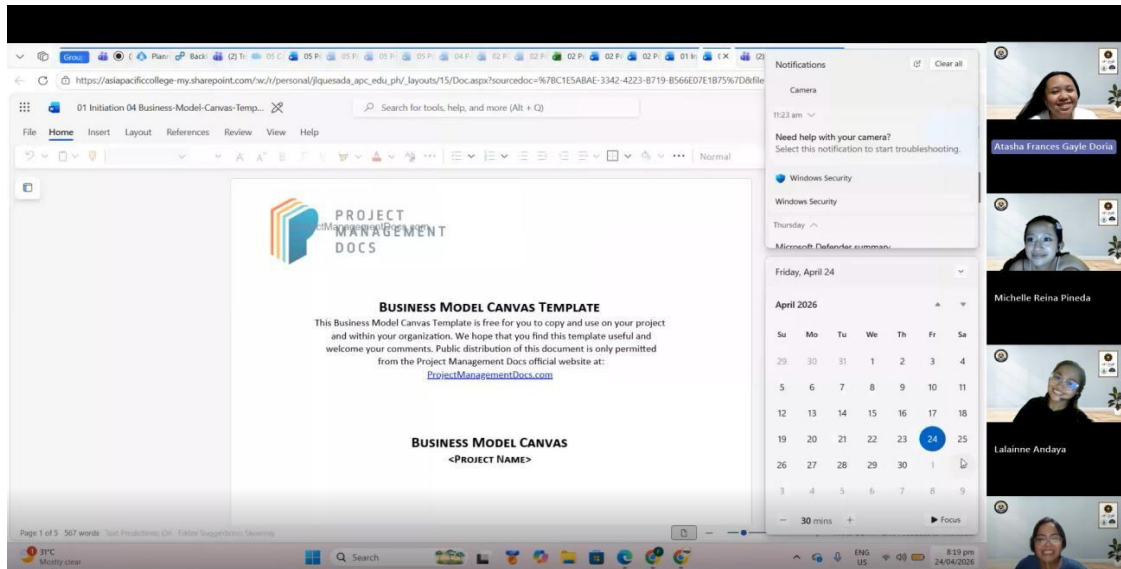


Meeting Link: [SPRINT 3-planning april 24, 2026-20260424 201839-Meeting Recording.mp4](#)

Action Items

- All members will work on their respective parts
- Add tasks inside work packages

LogiTeh Sprint 2 Outputs

Openproject Board

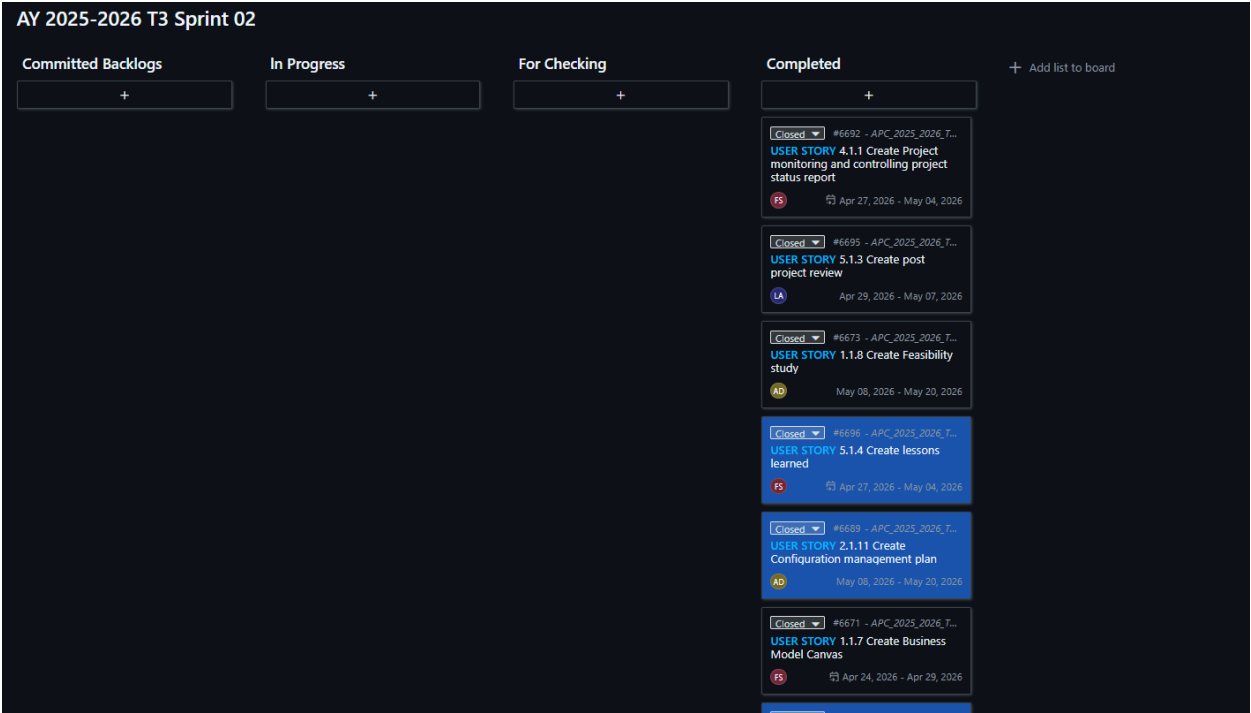

Assigned to Lalainne Andaya

6683	2.1.8 Create Project Risk Management Plan	USER STORY	Closed	LA Lalainne Andaya	Normal	-	Term 3 Sprint 2
6684	2.1.8.1 Create Risk Identification Framework	TASK	Closed	LA Lalainne Andaya	Normal	-	Term 3 Sprint 2
6685	2.1.8.2 Map the Risk Qualification & Scoring	TASK	Closed	LA Lalainne Andaya	Normal	-	Term 3 Sprint 2
6686	2.1.8.3 Contingency Planning	TASK	Closed	LA Lalainne Andaya	Normal	-	Term 3 Sprint 2
6690	2.1.12 Create change management plan	USER STORY	Closed	LA Lalainne Andaya	Normal	Planning	Term 3 Sprint 2
6778	2.1.12.2 Create impact analysis	TASK	Closed	LA Lalainne Andaya	Normal	-	Term 3 Sprint 2
6779	2.1.12.3 CCB coordination	TASK	Closed	LA Lalainne Andaya	Normal	-	Term 3 Sprint 2
5485	5.0 Closing Phase	PHASE	New	-	Normal	-	-
5486	5.1 Chapter 5 PM foundations closing a project	SUMMARY TASK	New	-	Normal	-	-
6695	5.1.3 Create post project review	USER STORY	Closed	LA Lalainne Andaya	Normal	-	Term 3 Sprint 2
6790	5.1.3.1 Compare the final Actual Cost to the Baseline Budget	TASK	Closed	LA Lalainne Andaya	Normal	-	Term 3 Sprint 2
6791	5.1.3.2 perform RCA on any project failure and identify best practices	TASK	Closed	LA Lalainne Andaya	Normal	-	Term 3 Sprint 2

Assigned to Atasha Frances Gayle Doria

LogiTech Sprint 2 Outputs

ID	SUBJECT	TYPE	STATUS	ASSIGNEE	PRIORITY	PROJECT PHASE	VERSION
5498	1.0 Initiation Phase	PHASE	New	-	Normal	Initiating	-
5500	1.1 PM Foundations Chapter 1: Initiate a Project	FEATURE	New	-	Normal	Initiating	-
6671	1.1.8 Create Feasibility study	USER STORY	Closed	AD Atasha Frances Gayle Doria	Normal	Initiating	Term 3 Sprint 2
6679	1.1.8.1 Technology & Infrastructure Evaluation	TASK	Closed	AD Atasha Frances Gayle Doria	Normal	Initiating	Term 3 Sprint 2
6680	1.1.8.2 Marketing & Sales Strategy	TASK	Closed	AD Atasha Frances Gayle Doria	Normal	Initiating	Term 3 Sprint 2
6681	1.1.8.3 HR & Organizational Planning	TASK	Closed	AD Atasha Frances Gayle Doria	Normal	Initiating	Term 3 Sprint 2
6682	1.1.8.4 Risk Analysis	TASK	Closed	AD Atasha Frances Gayle Doria	Normal	Initiating	Term 3 Sprint 2
5485	5.0 Closing Phase	PHASE	New	-	Normal	-	-
5486	5.1 Chapter 5 PM foundations closing a project	SUMMARY TASK	New	-	Normal	-	-
6694	5.1.2 Create Project acceptance	USER STORY	Closed	AD Atasha Frances Gayle Doria	Normal	-	Term 3 Sprint 2
6786	5.1.2.1 cross reference RIM and do Product Performance Evaluation	TASK	Closed	AD Atasha Frances Gayle Doria	Normal	Closing	Term 3 Sprint 2
6787	5.1.2.2 Operational Handover Completion	TASK	Closed	AD Atasha Frances Gayle Doria	Normal	-	Term 3 Sprint 2
6788	5.1.2.3 Administrative Closeout	TASK	Closed	AD Atasha Frances Gayle Doria	Normal	-	Term 3 Sprint 2
6789	5.1.2.4 Resource Release and Archiving	TASK	Closed	AD Atasha Frances Gayle Doria	Normal	-	Term 3 Sprint 2
5118	2.0 Planning Phase	PHASE	New	-	Normal	Initiating	Term 3 Sprint 0
5621	2.1 PM Foundations Chapter 2: Plan a Project	FEATURE	In progress	-	Normal	-	-
6689	2.1.11 Create Configuration management plan	USER STORY	Closed	AD Atasha Frances Gayle Doria	Normal	Planning	Term 3 Sprint 3
6775	2.1.11.1 Set up the CMDB and assign access levels	TASK	Closed	AD Atasha Frances Gayle Doria	Normal	Planning	Term 3 Sprint 2

Assigned to Feliz Salting

ID	SUBJECT	TYPE	STATUS	ASSIGNEE	PRIORITY	PROJECT PHASE	VERSION
5498	1.0 Initiation Phase	PHASE	New	-	Normal	Initiating	-
5500	1.1 PM Foundations Chapter 1: Initiate a Project	FEATURE	New	-	Normal	Initiating	-
6671	1.1.7 Create Business Model Canvas	USER STORY	Closed	FS Feliz Angelica Salting	Normal	Initiating	Term 3 Sprint 2
6674	1.1.7.1 Identify Customer Segments & Value Propositions	TASK	Closed	FS Feliz Angelica Salting	Normal	-	Term 3 Sprint 2
6675	1.1.7.2 Identify Key Partners, Map Key Activities, Audit Key Resources	TASK	Closed	FS Feliz Angelica Salting	Normal	-	Term 3 Sprint 2
6676	1.1.7.3 Determine how the product will reach customers	TASK	Closed	FS Feliz Angelica Salting	Normal	-	Term 3 Sprint 2
6677	1.1.7.4 Check financial viability	TASK	Closed	FS Feliz Angelica Salting	Normal	-	Term 3 Sprint 2
5484	4.0 Monitoring and Controlling	PHASE	Closed	-	Normal	-	-
6691	4.1 Chapter 4 PM Foundations monitor and control a project	FEATURE	Closed	-	Normal	-	-
6692	4.1.1 Create Project monitoring and controlling project status report	USER STORY	Closed	FS Feliz Angelica Salting	Normal	-	Term 3 Sprint 2
6780	4.1.1.1 define the RAG criteria, EVM, and KPI	TASK	Closed	FS Feliz Angelica Salting	Normal	-	Term 3 Sprint 2
6781	4.1.1.2 Track Weekly/Monthly Status	TASK	Closed	FS Feliz Angelica Salting	Normal	-	Term 3 Sprint 2
5485	5.0 Closing Phase	PHASE	New	-	Normal	-	-
5486	5.1 Chapter 5 PM foundations closing a project	SUMMARY TASK	New	-	Normal	-	-
6696	5.1.4 Create lessons learned	USER STORY	Closed	FS Feliz Angelica Salting	Normal	-	Term 3 Sprint 2
6793	5.1.4.1 Analyze both realized and unrealized risks	TASK	Closed	FS Feliz Angelica Salting	Normal	-	Term 3 Sprint 2
6794	5.1.4.2 Analyze gaps in current processes	TASK	Closed	FS Feliz Angelica Salting	Normal	-	Term 3 Sprint 2

Assigned to Michelle Pineda

ID	SUBJECT	TYPE	STATUS	ASSIGNEE	PRIORITY	PROJECT PHASE	VERSION
5485	5.0 Closing Phase	PHASE	New	-	Normal	-	-
5486	5.1 Chapter 5 PM foundations closing a project	SUMMARY TASK	New	-	Normal	-	-
5487	5.1.1 Create transition out plan	USER STORY	New	MP Michelle Pineda	Normal	-	Term 3 Sprint 2
6782	5.1.1.1 setup strategy for transition	TASK	Closed	MP Michelle Pineda	Normal	-	Term 3 Sprint 2
6783	5.1.1.2 knowledge transfer and training	TASK	Closed	MP Michelle Pineda	Normal	-	Term 3 Sprint 2
6784	5.1.1.3 Technical and Property Asset Transfer	TASK	Closed	MP Michelle Pineda	Normal	-	Term 3 Sprint 2
6785	5.1.1.4 Formal Handover and Acceptance	TASK	Closed	MP Michelle Pineda	Normal	-	Term 3 Sprint 2
5118	2.0 Planning Phase	PHASE	New	-	Normal	Initiating	Term 3 Sprint 0
5621	2.1 PM Foundations Chapter 2: Plan a Project	FEATURE	In progress	-	Normal	-	-
6687	2.1.9 Create Requirements Management Plan	USER STORY	Closed	MP Michelle Pineda	Normal	Planning	Term 3 Sprint 2
6769	2.1.9.1 Identify the requirements	TASK	Closed	MP Michelle Pineda	Normal	-	Term 3 Sprint 2
6770	2.1.9.2 define requirements acceptance criteria	TASK	Closed	MP Michelle Pineda	Normal	-	Term 3 Sprint 2
6771	2.1.9.3 Draft Requirements Traceability Matrix (RTM)	TASK	Closed	MP Michelle Pineda	Normal	-	Term 3 Sprint 2
6772	2.1.9.4 Traceability Testing	TASK	Closed	MP Michelle Pineda	Normal	-	Term 3 Sprint 2
6688	2.1.10 Create Risk register	USER STORY	Closed	MP Michelle Pineda	Normal	Planning	Term 3 Sprint 2
6773	2.1.10.1 Standardize Risk Syntax and Conditional Formatting	TASK	Closed	MP Michelle Pineda	Normal	Planning	Term 3 Sprint 2
6774	2.1.10.2 consult with devs for scoring entries	TASK	Closed	MP Michelle Pineda	Normal	Planning	Term 3 Sprint 2

LogiTech Sprint 2 Outputs

Daily Standup Outputs

April 27, 2026, DSU

The screenshot shows a Microsoft Teams meeting interface. At the top, there's a toolbar with icons for Pop out, Chat, People (4), Raise, React, View, More, Camera, Mic, and Share. Below the toolbar, four video thumbnails of participants are visible. The main area shows a shared screen of a document titled 'LogiTech, 01 Project Initiative 04 Business Model Canvas - Saved'. The document is a business model canvas for 'Furlink'. It includes sections for 'Project', 'Value Proposition', 'Channels', and 'Customer Segments'. The 'Project' section describes the goal of building a centralized digital booking platform for the pet care market. The 'Value Proposition' section lists benefits like 24/7 inquiries and AI booking assistance. The 'Channels' section mentions the application admin and service provider applications. The 'Customer Segments' section identifies target customers like pet owners and groomers. The document also includes a 'KEY RESOURCES' section and a 'What are the...' section. The bottom of the screen shows the Windows taskbar with various application icons.

Meeting Link: [DSU April 27, 2026-20260427_193413-Meeting Recording.mp4](#)

Action Items

- All members will continue to work on their respective parts
- Prepare for the questions that will be consulted to our adviser

LogiTech Sprint 2 Outputs

Forum

Replies (4)

LA

RE: Sprint 2 Week 9 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Lalainne Andaya 1 day ago

1. What did I do yesterday?
 - I updated the milestone, risk management plan, and project change management plan
2. What will I do today?
 - Update budget and start on post project review document
3. Anything blocking I progress?
 - No blockers

FS

RE: Sprint 2 Week 9 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Feliz Angelica Salting about 14 hours ago

1. What did I do yesterday? I updated the schedule management approach
2. What will I do today? I will start working on the scope change section
3. Anything blocking I progress? none

MP

RE: Sprint 2 Week 9 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Michelle Pineda about 10 hours ago

1. What did I do yesterday?
 - I worked on the requirements management plan
2. What will I do today?
 - Continue on the requirements traceability and start risk register
3. Anything blocking I progress?
 - None

AD

RE: Sprint 2 Week 9 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Atasha Frances Gayle Doria about 9 hours ago

1. What did I do yesterday?
 - Started doing the Feasibility Study and Project Acceptance.
2. What will I do today?
 - Do all the revision and finish the Feasibility Study and Project Acceptance
3. Anything blocking I progress?
 - The cost figure part in feasibility study since I am waiting for the costing.

LogiTech Sprint 2 Outputs

April 29, 2026, DSU

The screenshot shows a Microsoft Teams meeting interface. At the top, the title bar reads "Meeting in *G03 LogiTech*" and the participant list includes "Asia Pacific College". Below the title bar is a toolbar with icons for Pop out, Chat, People, Raise, React, View, More, Camera, Mic, Share, and Leave. The main area displays four video thumbnails of participants. Below the thumbnails, a shared screen shows a document titled "Business Model Canvas". The canvas is divided into several sections: KEY PARTNERS, KEY ACTIVITIES, VALUE PROPOSITIONS, CUSTOMER RELATIONSHIPS, CUSTOMER SEGMENTS, KEY RESOURCES, and CHANNELS. The text within these sections describes a pet care platform, including details about API integration, platform development, and various services like pet sitting and dog walking. A watermark "teams.cloud.microsoft is sharing your screen" is visible across the canvas. At the bottom of the screen, the name "Feliz Angelica Salting" is displayed, along with a "Show hidden icons" button.

Meeting Link: [DSU April 29, 2026-20260429_202445-Meeting Recording.mp4](#)

Action Items

- All members will continue to work on their respective parts
- Prepare for the questions that will be consulted to our adviser.

LogiTech Sprint 2 Outputs

Forum

LA

RE: Sprint 2 Week 9 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Lalainne Andaya 1 day ago

1. What did I do yesterday?
 - I updated the budget and started working on post project review
2. What will I do today?
 - Complete post project review and help with cost feasibility
3. Anything blocking I progress?
 - No blockers

FS

RE: Sprint 2 Week 9 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Feliz Angelica Salting about 13 hours ago

1. What did I do yesterday? Tracked milestone and deliverables for project status report
2. What will I do today? Continue KPI tracking
3. Anything blocking I progress? none

MP

RE: Sprint 2 Week 9 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Michelle Pineda about 10 hours ago

1. What did I do yesterday?
 - I started the requirements management plan
2. What will I do today?
 - Continue on the requirements management plan
3. Anything blocking I progress?
 - None

AD

RE: Sprint 2 Week 9 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Atasha Frances Gayle Doria about 9 hours ago

1. What did I do yesterday?
 - Started doing the Configuration Management Plan
2. What will I do today?
 - Revise the Feasibility, Project Acceptance, and Configuration Plan and updated the midterm document.
3. Anything blocking I progress?
 - The cost figure part in feasibility.

LogiTech Sprint 2 Outputs

May 4, 2026 DSU



Meeting Link: [DSU May 4, 2026 Meeting Recording.mp4](#)

Action Items

- All members will continue to work on their respective parts

LogiTech Sprint 2 Outputs

Forum

LA

RE: Sprint 2 Week 10 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Lalainne Andaya 1 day ago

1. What did I do yesterday?
 - Added recommendations on the project post review
2. What will I do today?
 - Complete other remaining parts of the project post review
3. Anything blocking I progress?
 - No blockers

FS

RE: Sprint 2 Week 10 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Feliz Angelica Salting about 14 hours ago

1. What did I do yesterday? I continued on identifying the key partners and activities
2. What will I do today? I will continue figuring out the value propositions
3. Anything blocking my progress? none

MP

RE: Sprint 2 Week 10 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Michelle Pineda about 10 hours ago

1. What did I do yesterday?
 - I worked on the risk register and transition out plan
2. What will I do today?
 - Finish risk register and transition out plan
3. Anything blocking I progress?
 - None



AD

RE: Sprint 2 Week 10 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Atasha Frances Gayle Doria about 10 hours ago

1. What did I do yesterday?
 - Revise the Project Acceptance and Configuration Plan and updated the midterm document.
2. What will I do today?
 - Compute for the cost figures.
3. Anything blocking I progress?
 - No blockers.

LogiTech Sprint 2 Outputs

May 7, 2026 DSU

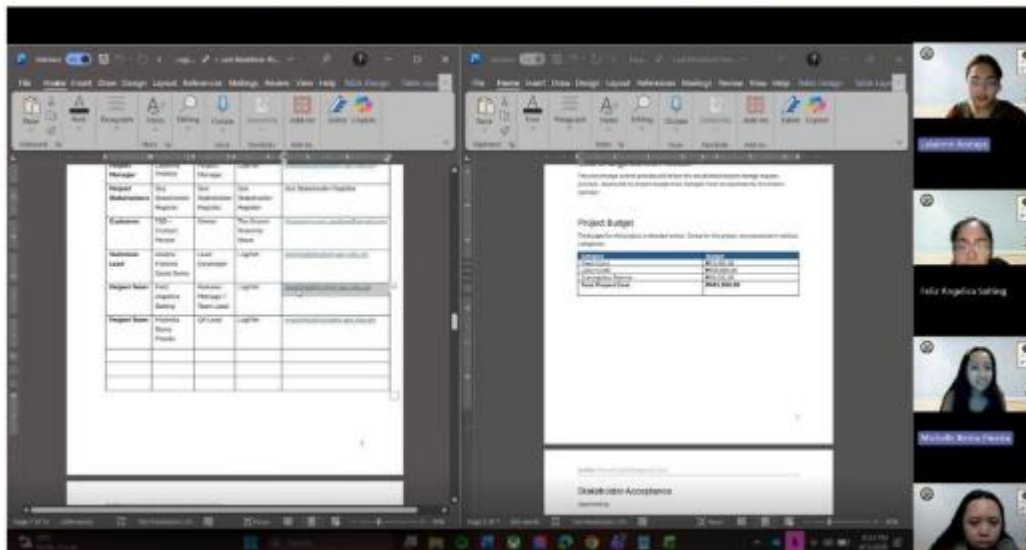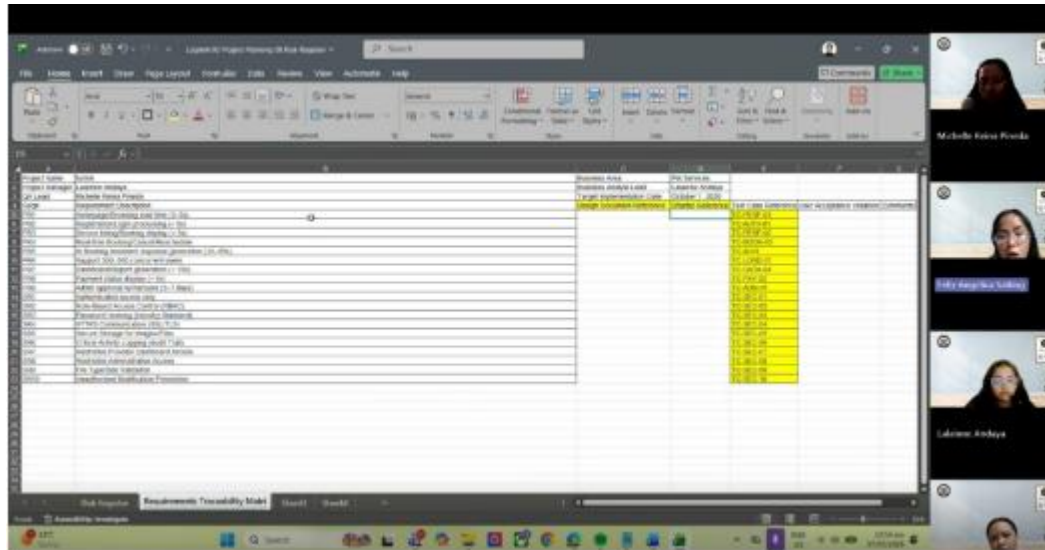

Meeting Link: [DSU April 29, 2026-20260429_202445-Meeting Recording.mp4](#)

Action Items

- All members will continue to work on their respective parts

LogiTech Sprint 2 Outputs

Forum

LA

RE: Sprint 2 Week 10 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Lalainne Andaya 1 day ago

1. What did I do yesterday?
 - Completed recommendations and transition to operations in project post review
2. What will I do today?
 - Finish project costs and project deliverables
3. Anything blocking my progress?
 - No blockers

FS

RE: Sprint 2 Week 10 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Feliz Angelica Salting about 14 hours ago

1. What did I do yesterday?
 - I finished the business model canvas focused on the customer segments
2. What will I do today?
 - I will proceed to starting project status report
3. Anything blocking my progress?
 - No blockers

MP

RE: Sprint 2 Week 10 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Michelle Pineda about 10 hours ago

1. What did I do yesterday?
 - I worked on completing all the three documents assigned to me
2. What will I do today?
 - check all documents if anything needs revision
3. Anything blocking I progress?
 - None


AD

RE: Sprint 2 Week 10 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Atasha Frances Gayle Doria about 10 hours ago

1. What did I do yesterday?
 - Computed for the cost figures.
2. What will I do today?
 - Revisit and finalize documents.
3. Anything blocking I progress?
 - No blockers.


LogiTeh Sprint 2 Outputs

Backlog Refinement

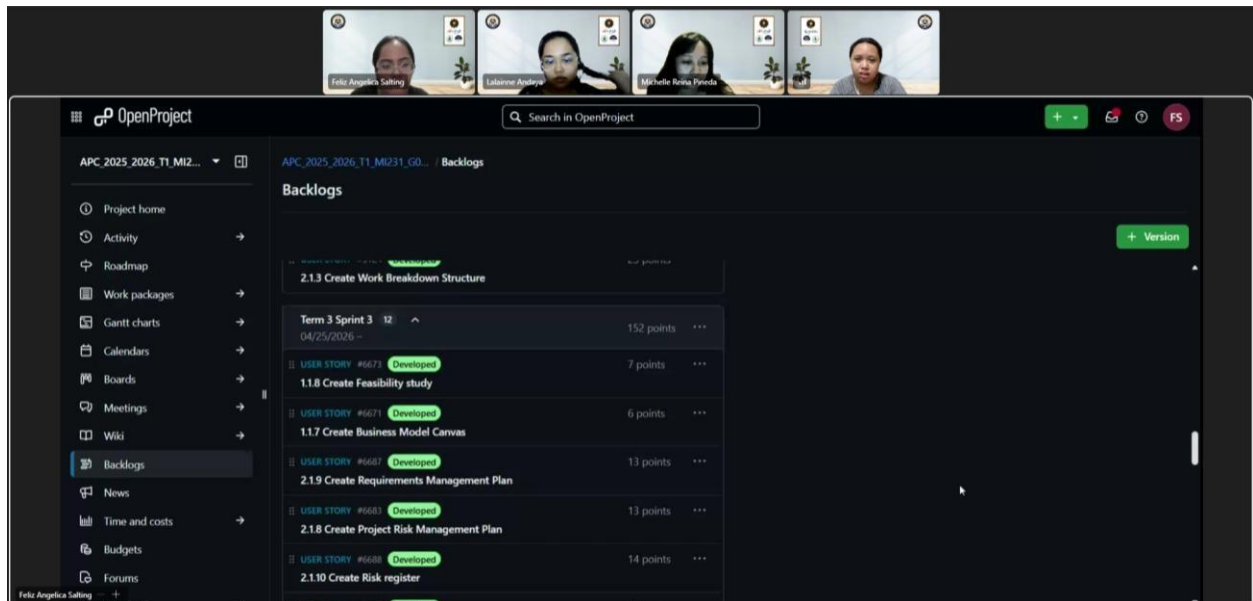

Sprint Backlog Refinement Link

OpenProject Board

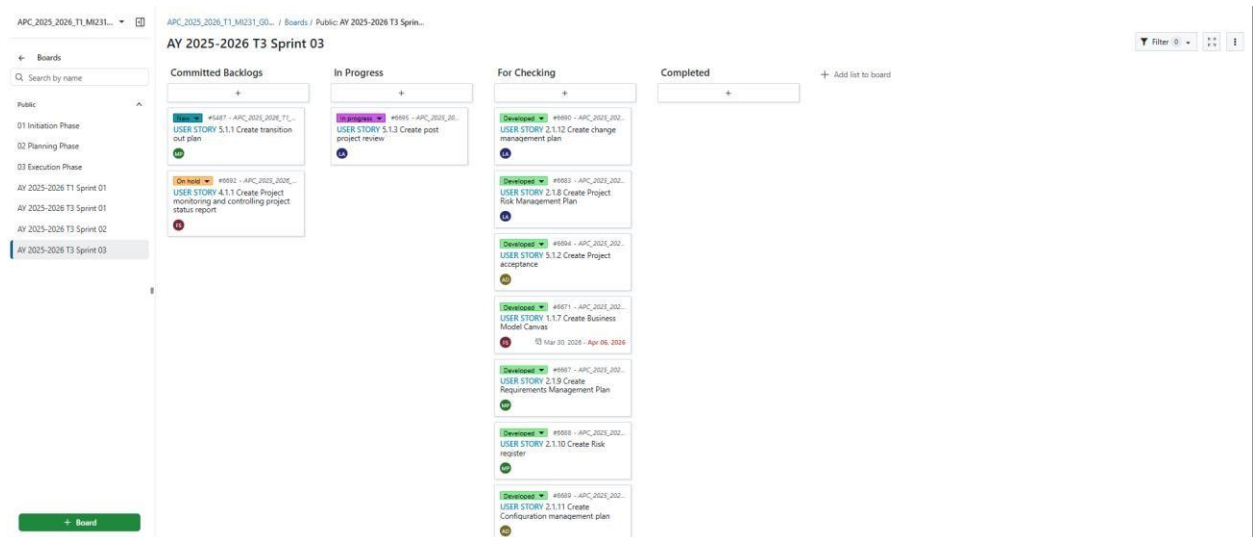

LogiTech Sprint 2 Outputs

Sprint Review

LogiTech-01 Interaction 01 Feasibility Study

File Home Insert Design Layout References Mailings Review View Help

Clipboard Font Paragraph Styles Editing Comments Share

LogiTech will currently operate under a non-monetized pilot phase (version 1.0 to 2.1) to eliminate barriers to entry, validate system workflow, and build a trusted community. Upon transitioning to commercial operations, the platform will introduce two primary revenue streams:

- **Transaction-Based Booking Fee:** LogiTech will generate revenue by collecting a booking fee from each successfully completed grooming appointment facilitated through the platform. The fee structure and percentage are to be finalized based on market research and user feedback gathered during the pilot phase.
- **Featured Provider Campaigns:** LogiTech will offer service providers the opportunity to participate in paid promotional campaigns. Participating providers will be featured prominently within the platform and included in LogiTech's social media marketing activities, giving their businesses increased visibility to pet owners. This program is

7

opt-in and voluntary, allowing providers to choose whether to invest in additional exposure based on their own business goals.

Cost Figures

Detailed cost figures including infrastructure, operational, and marketing expenses are currently being finalized. This section will be updated with a complete financial projection.

Page 13 of 14 2784 words English (Philippines) Accessibility: Investigate

Michelle Reina Pineda

Atasha Frances Gayle Doria

Lalaine Andaya

Feliz Angelica Salting

1:41 pm 07/05/2025

Meeting Link: [Sprint Review Meeting Link](#)

LogiTech Sprint 2 Outputs

Burndown Chart



Sprint Retrospective

The screenshot shows a Confluence page for a sprint retrospective. The page is titled 'LogiTech / SPRINT RETRO 2026-07-05' and contains several sticky notes organized into columns. The notes are color-coded: pink for 'Liked', purple for 'Disliked', and blue for 'Wish'. The video call overlay on the right shows four participants: Michelle Reina Pineda, Atasha Frances Gayle Doria, Feliz Angelica Salting, and a fourth participant whose name is partially obscured.

Liked (Pink Notes):

- I liked our communication
- I liked our communication
- I liked how smooth sailing the sprint was

Disliked (Purple Notes):

- at the end of the sprint
- I like the pace we have
- I like the communication

Wish (Blue Notes):

- I wish we could have more communication with our project adviser
- I wish that we can maintain close communication with our project adviser
- I wish to push the APIs we'll be needing for our execution
- I wish to continue how we work as a team
- I wish to correctly deliver the documents
- I wish that we are able to stick with our schedule
- I wish to maintain our team dynamics
- I wish our plans included in the document will happen

Other Notes:

- development/testing phase will be smooth sailing
- I wish that we stick to the set schedule
- service providers like our product
- will happen during our development phase
- will be the feedback of our sprint
- I wonder if service provider like our initial deployment
- I wonder how we'll still be able to communicate effectively with stakeholders
- I wonder if the app that will onboard is satisfied with our system
- I wonder how
- I wonder what reactions we will get with the current planned improvements of further
- I wonder how will users adapt to our system

Sprint Retrospective Meeting Link

LogiTech Sprint 2 Outputs

Sprint Retrospective Board



Action Items:

- Polish API for execution phase
- Reach out to SP about training and onboarding
- Polish PMBOK documents from midterms to finals
- Continue development and adhere to schedule
